Operator: Aera Energy LLC
Well: TAY711
Type: Injector
Wellbore: 00
API : 0411121506

Wellbore Schematic

Datum: DERRICK FLOOR @ 267.00ft (default)
Ground Elev: 245.00ft
PBMD: 22ft
TD MD: 7,308ft
Orientation: Directional
Spud / KO Date: 4/26/1988

1/27/2021 ABANDONED

CASING

Size(in)	Top MD(ft)	Base MD(ft)
16.0000	22	50.0
9.6250	22	644.0
7.0000	22	7,300.0

CEMENT STAGES

Job Type: Primary Date: 4/27/1988

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
9.6250		22	644

Job Type: Primary Date: 5/10/1988

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000		22	7,300

Job Type: Plug Date: 2/25/2008

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	5,702	5,756

Job Type: Plug Date: 1/18/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	6,602	7,308

Job Type: Plug Date: 1/20/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	5,750	6,569

Job Type: Plug Date: 1/21/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	5,623	5,750

Job Type: Plug Date: 1/25/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	5,469	5,623
7.0000	6.2760	5,012	5,469

Job Type: Plug Date: 1/26/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	4,537	5,012
7.0000	6.2760	942	4,537

Job Type: Plug Date: 1/27/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	6.2760	625	942
7.0000	6.2760	22	625

Job Type: Primary Date: 1/27/2021

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000		22	600

REMARKS

BJ TITAN PUMPED 35 BBL WATER AHEAD OF 175 CU.FT. (67 SKS) 1:1:6 ¢G', DIAMIX, GEL WITH 2% CACL2 AND .25#/SK CELLOFLAKE. TAILED IN 175 CU.FT. (154 SKS) ¢G' WITH 3% CACL2. DROPPED PLUG AND DISPLACED CMT WITH 47 BBL MUD AT 7 BBL/MIN. BUMPED PLUG AT 1000 PSI, RELEASED TO ZERO, FLOAT HELD. CIP AT 11:30 AM 04/27/88 TRACE OF CMT TO SURFACE.

RUN 169 JTS.7" 26# K55 LTC. CSG. [7306.72'] SHOE @ 7300 FLOAT @ 7214 CIRC. HOWCO PUMPED 25 BBL H20 25 BBL SUPER FLUSH 5 BBL H20 1525 CF. CLASS G CMT W/ 16% GEL .8% CFR2 .4% HR7 & 950 CF. CLASS G CMT. W/ .5% HALAD 322 .5% HALAD 9 & 5% KCL. DISPLACE W/ 1562 CF. H20. LOST CIRC. LAST 1000 CF. DID NOT BUMP PLUG. NO CMT. RETURNS. FLOAT HE LD FILL HOLE. WOC. SET SLIPS. ETOC~ SURFACE..

Plug: 7" casing plugged at 5756' to 5702' with 14.47 sks of Standard Blend G cement at 14.2 ppg, with yield of 1.52 cf/sk.

Plug: 7" casing plugged at 7308' to 6602' with 100.32 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.

Plug: 7" casing plugged at 6569' to 5750' with 136.84 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.

Plug: 7" casing plugged at 5750' to 5623' with 21.05 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.

Plug: 7" casing plugged at 5469' to 5012' with 66.44 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.
Plug: 7" casing plugged at 5623' to 5469' with 25.65 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.

Plug: 7" casing plugged at 4537' to 942' with 513.15 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.
Plug: 7" casing plugged at 5012' to 4537' with 72.36 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.

Plug: 7" casing plugged at 625' to 22' with 100 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.
Plug: 7" casing plugged at 942' to 625' with 48.02 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk.

Plug: 7" x .625" casing (annulus) cemented at 600' to 22' with 70.39 sks of Standard Blend G cement at 15.6 ppg, with yield of 1.52 cf/sk. .1 bbls of cement returns to surface.

Initials: DM Date: 3/29/2021

ABANDONMENT

Abandonment Tag Depth: 7,308.00ft

UIC Project Code(s)

UIC: 8140017 Pool 10 Zone:A3/B2B/B3 Top: 4481' Bot:5515'
UIC: 8140021 Pool 35 Zone:C2/C3/C4(E) Top 5515' Bot:7308'
UIC: 8140018 Pool 40 Zone: C3/C4(W) Top 5515' Bot:7308'

BASE OF USDW

Base MD (ft) N/A

BASE OF FRESH WATER

Base MD (ft) N/A

PERFORATIONS

Top MD(ft)	Bottom MD(ft)	Density(shot/ft)
600.00	600.00	1.00
620.00	620.00	1.00
5,755.00	5,820.00	1.00
5,830.00	5,915.00	1.00
5,960.00	6,000.00	4.00
6,010.00	6,040.00	4.00
6,080.00	6,128.00	1.00
6,138.00	6,190.00	1.00
6,610.00	6,640.00	4.00
6,650.00	6,670.00	4.00
6,680.00	6,780.00	4.00
6,810.00	6,830.00	4.00
6,852.00	7,010.00	4.00
7,020.00	7,150.00	4.00
7,160.00	7,200.00	4.00

PLUG DETAILS

Assembly name: PLUG

Type	Top MD(ft)	Btm MD(ft)
Cement Plug	22	625
Cement Plug	625	942

Assembly name: PLUG

Type	Top MD(ft)	Btm MD(ft)
Cement Plug	942	4,537
Cement Plug	4,537	5,012

Assembly name: PLUG

Type	Top MD(ft)	Btm MD(ft)
Cement Plug	5,012	5,469
Cement Plug	5,469	5,623

Assembly name: PLUG

Type	Top MD(ft)	Btm MD(ft)
Cement Plug	5,623	5,750

Assembly name: PLUG

Type	Top MD(ft)	Btm MD(ft)
Cement Plug	5,750	6,569

Assembly name: FISH

Type	Top MD(ft)	Btm MD(ft)
Tubing	6,569	6,575
Packer	6,575	6,581
Profile Nipple	6,581	6,582

Assembly name: PLUG

Type	Top MD(ft)	Btm MD(ft)
Mud	6,569	6,602

Assembly name: PLUG


Type	Top MD(ft)	Btm MD(ft)
Cement Plug	6,602	7,308

Assembly name: Other Plug

Type	Top MD(ft)	Btm MD(ft)
OTHER PLUG	7,300	7,308

MARKER DETAILS

Name	MD top(ft)
A-1	881.00
A-2	3,328.00
A-3	4,481.00
B-2	4,812.00
B-3	4,835.00
C-2	5,515.00
C-3	5,756.00
C-4	6,767.00

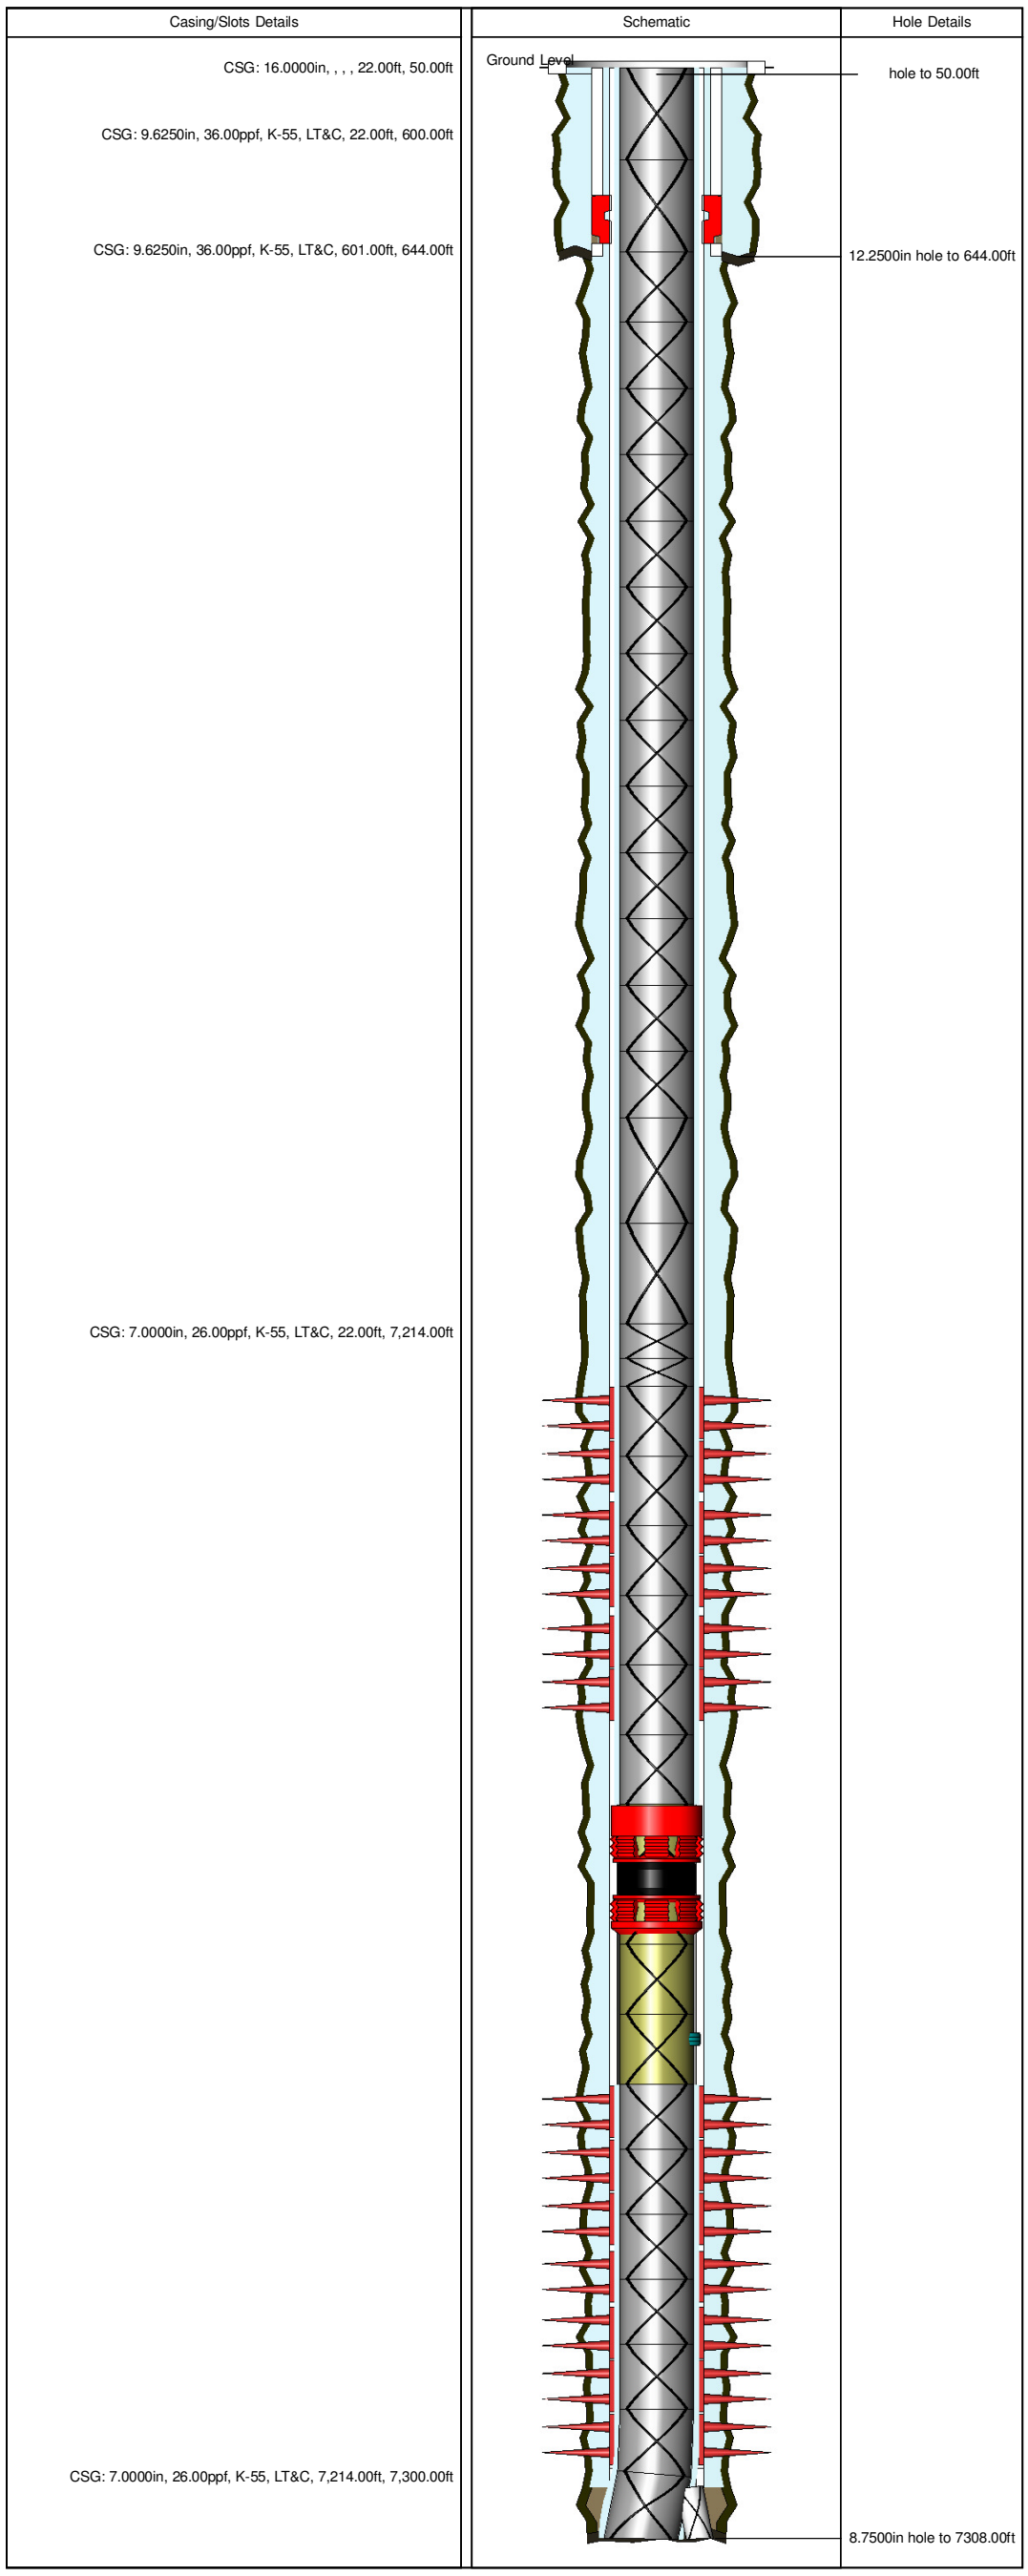

Obstruction	Comments	OD(in)	Top MD(ft)	Base MD(ft)
OBSTRUCTION	On 2/26/08. RIH w/ milling assembly on 2-7/8" tbg. 6.151" O.D. watermelon mills & 6-1/8" bit. Mills stacked out @ 3,107'. Unable to work past 3,107'. On 2/27/08. Tripped 5.969" O.D. watermelon mills w/ 3-5/8" mule shoe, 2-7/8" fatigue nipple below mills. Tallied, RIH w/ watermelon mills assembly, (4) 4-3/4" drill collars on 2-7/8" tbg. Felt slight bobble @ 3,107'. Worked watermelon mills through 3,107' reciprocated numerous times. Continued to RIH w/ 2-7/8" tbg & tagged TOC @ 5,700'.		3,107.00	3,107.00
DAMAGED CSG.	On 2/22/08. Possible parted casing @ 5,754'.		5,754.00	5,754.00
OBSTRUCTION	On 9/25/06. Tagged w/ 4" & 5-1/4" IB @ 5,774', IB's indication were both inconclusive.		5,771.00	5,774.00
FISH	On 8/29/06. Chemical cut tbg @ 6,569' (5') above bottom packer. Left fish in wellbore 2.2500 6,569' T/ 6,581.82'. Fish detail as follows; approximately 5.82' x 2.875" tbg, 6' x 7" UP-6 packer,1' profile nipple.		6,569.00	6,581.82
