
Wellbore Diagram

Well Name: MC G-7A **API: 0403045716**

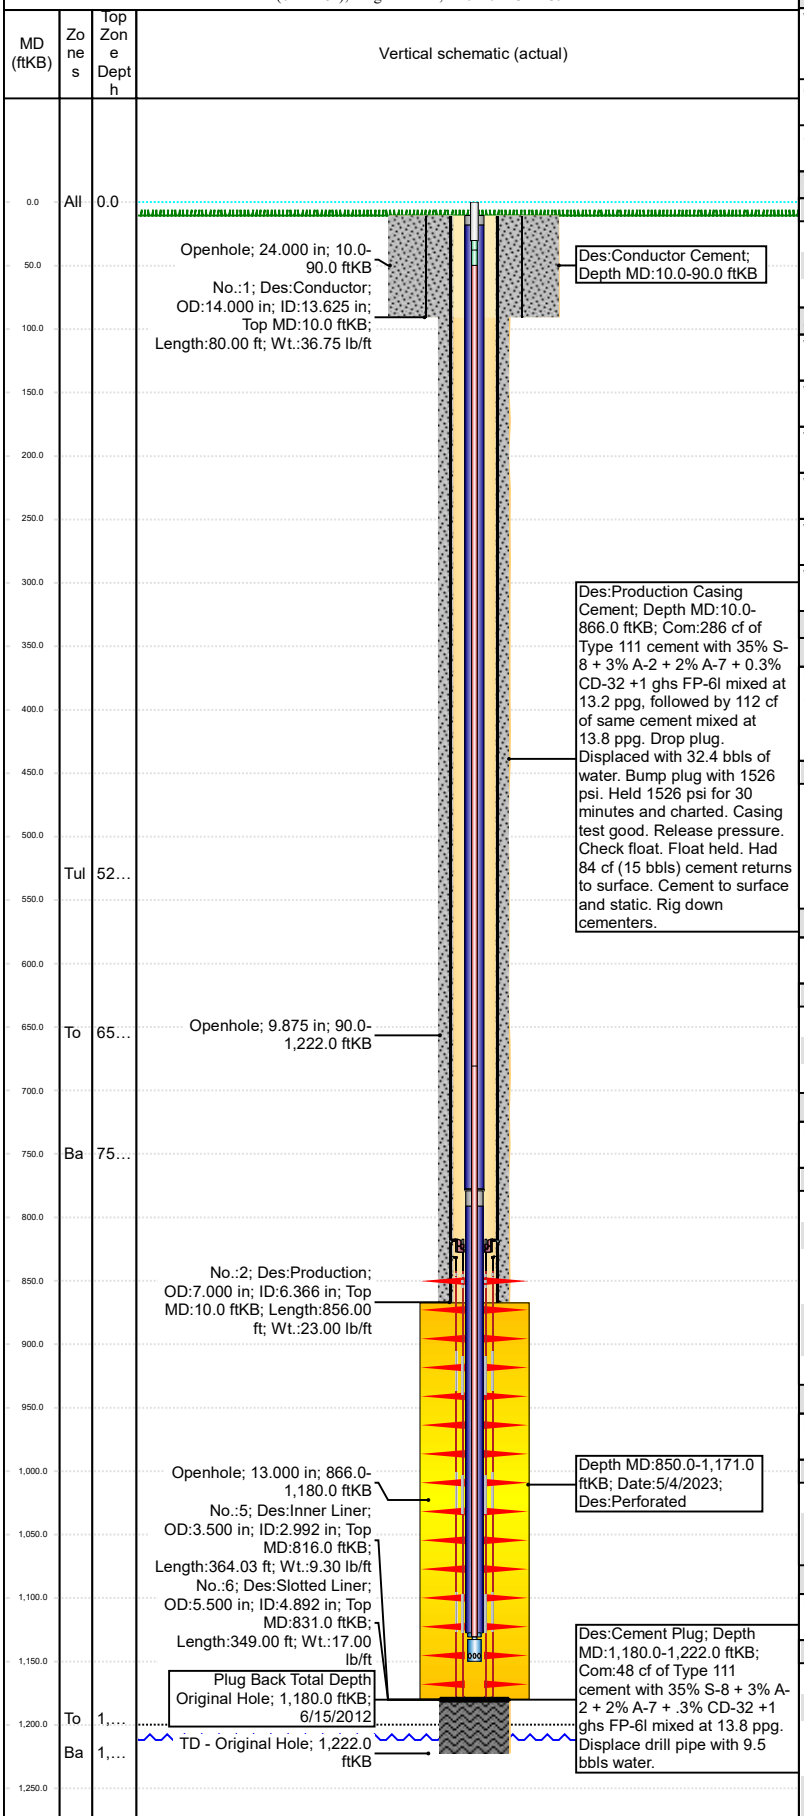

Well Header Setup

Well Name	Field Name	API/UWI (10)	PBTD (ftKB)	TD (max) (ftKB)
MC G-7A	MC RPT	0403045716	Original Hole - 1,180.0	1,222.0

Gr Elev (ft)	KB-Grd (ft)	Spud Date	Rig Release Date	Abandon Date
1,198.13	10.00	6/14/2012	6/17/2012	

Section	Township	Range	Meridian	Latitude (NAD 27) (°)	Longitude (NAD 27) (°)	Datum
24	31S	22E	MD	35.2099952700	-119.5590057400	NAD 83

WELLBORE SECTIONS

Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Openhole	24	10.0	90.0
Openhole	9 7/8	90.0	1,222.0
Openhole	13	866.0	1,180.0

Zones

Wellbore Name	Zone Name	Top Depth (ftKB)	Reference Depth (ftKB)
Original Hole	Alluvium	0.0	
Original Hole	Tulare	528.7	0.0
Original Hole	Top Upper CL	654.1	
Original Hole	Base Upper CL	750.3	
Original Hole	Top Lower CL	1,194.3	
Original Hole	Base Lower CL	1,221.8	

CASING DATA

Conductor

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
4/6/2012	14	13.63	0.25" WallA53B/A106	36.75	10.0	90.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Conductor	14.000	13.625	80.00	0.25" Wall A53 B/A106	36.75	10.0	90.0

Production

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
6/15/2012	7	6.37	J-55	23.00	10.0	866.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Casing Joints	7.000	6.366	808.00	J-55	23.00	10.0	818.0
Insert	7.000	6.366	1.00	J-55	23.00	818.0	819.0
Casing Joints	7.000	6.366	47.00	J-55	23.00	819.0	866.0

Inner Liner

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
7/8/2021	3 1/2	2.99	J-55	9.30	790.0	1,171.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
SSA	3.500	2.992	10.00	J-55	9.30	790.0	800.0
Blank Liner	3.500	2.992	30.00	J-55	9.30	800.0	830.0
Slotted Liner (Simi Slots)	3.500	2.992	31.00	J-55	9.30	830.0	861.0
Slotted Liner (Full Slots)	3.500	2.992	308.00	J-55	9.30	861.0	1,169.0
Shoe	3.500	2.992	2.00	J-55	9.30	1,169.0	1,171.0

Old Inner Liner

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
11/16/2020	3 1/2	2.99	J-55	9.30	808.0	1,173.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
SSA	3.500	2.992	1.00	J-55	9.30	808.0	809.0
Slotted Liner (Full Slots)	3.500	2.992	364.00	J-55	9.30	809.0	1,173.0

Inner Liner


Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
5/23/2024	3 1/2	2.99	J-55	9.30	816.0	1,180.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
SSA	3.500	2.992	11.94			816.0	827.9
Blank Liner	3.500	2.992	15.05	J-55	9.30	827.9	843.0
Slotted Casing	3.500	2.992	15.03	J-55	9.30	843.0	858.0
Slotted Casing	3.500	2.992	319.86	J-55	9.30	858.0	1,177.9

Wellbore Diagram

Well Name: MC G-7A **API: 0403045716**

Vertical (0° to 15°), Original Hole, 12/9/2024 3:42:40 PM

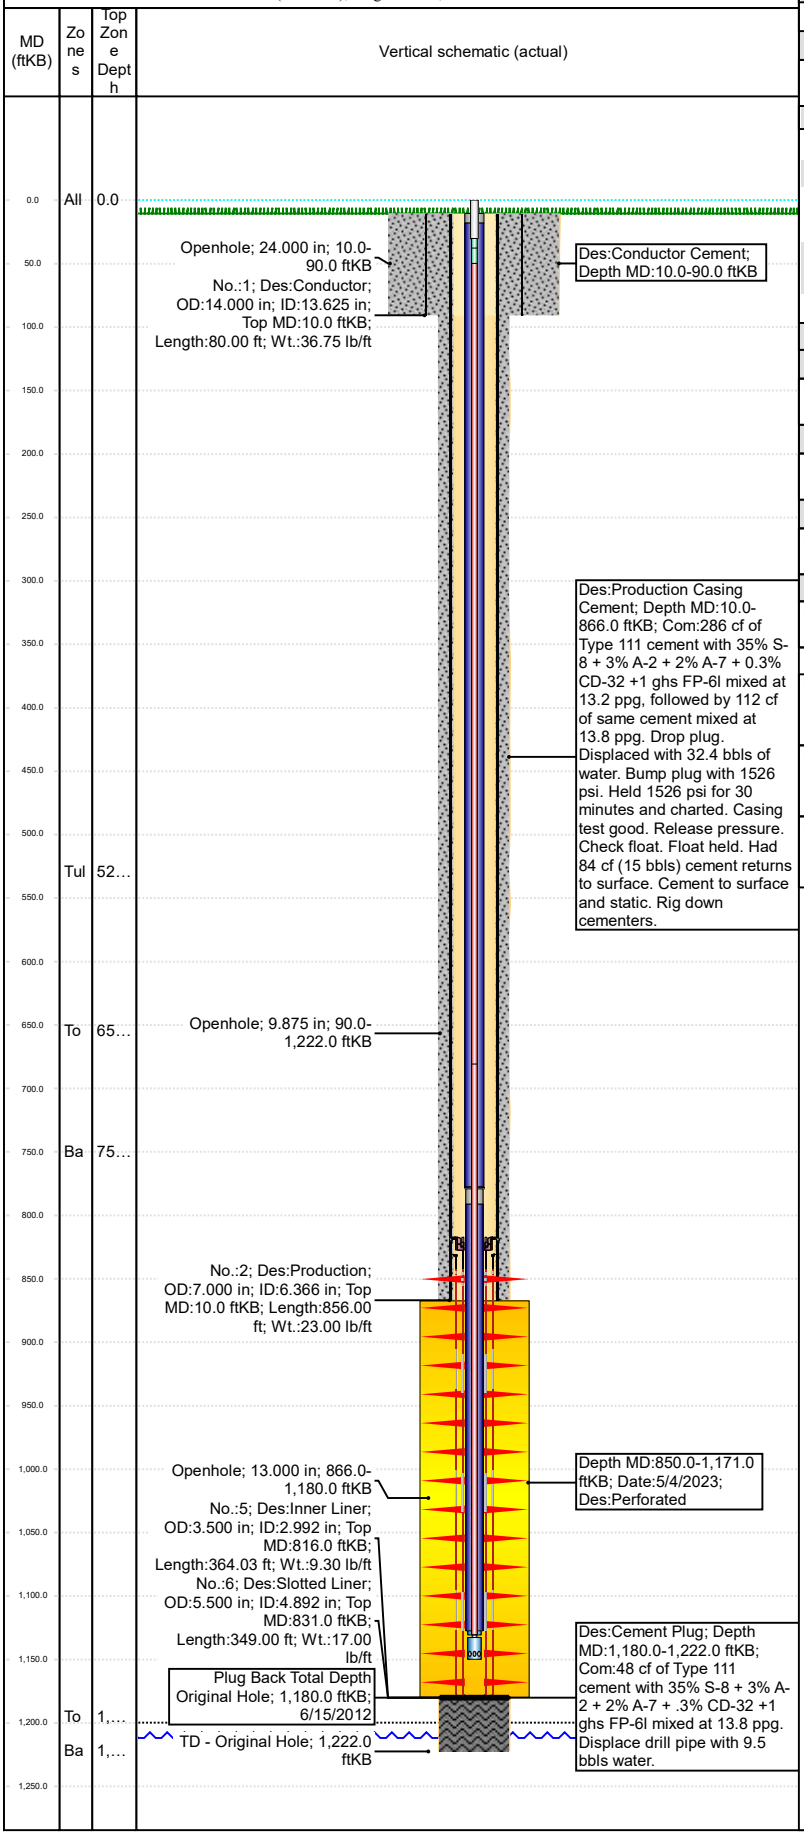

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Shoe	3.500	2.992	2.15	J-55	9.30	1,177.9	1,180.0

Slotted Liner

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
6/16/2012	5 1/2	4.89	J-55	17.00	831.0	1,180.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
SSA	5.500	4.892	1.00	J-55	17.00	831.0	832.0
Blank Liner	5.500	4.892	11.00	J-55	17.00	832.0	843.0
Slotted Liner (Simi Slots)	5.500	4.892	10.00	J-55	17.00	843.0	853.0
Slotted Liner (Full Slots)	5.500	4.892	326.00	J-55	17.00	853.0	1,179.0
Guide Shoe	5.500	4.892	1.00	J-55	17.00	1,179.0	1,180.0

CEMENT DATA

Conductor , 90.0 ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full Ret…	Vol…
Conductor Cement	Casing	10.0	90.0	No	0.0

<Casing Description?>, 1,222.0 ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full Ret…	Vol…
Cement Plug	Plug	1,180.0	1,222.0	No	0.0

Production , 866.0 ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full Ret…	Vol…
Production Casing Cement	Casing	10.0	866.0	Yes	15.0

PERFORATION DATA

Date	Type	Top (ftKB)	Btm (ftKB)	Entered Sho…	Calculated…	Comment
5/4/2023	Perforated	850.0	1,171.0		1,285	

Other In Hole

Des	OD (in)	ID (in)	Top (ftKB)	Btm (ftKB)	Comment
Gravel packs	13	5.50	866.0	1,180.0	250 cf of 16x30 mesh gravel in place.
Gravel packs	3 1/2		803.0	1,173.0	32 cf of Carbolite 20/40
Gravel packs	3 1/2		830.0	1,171.0	56 cf of 8/12 Natural gravel in place
