WELLBORE DIAGRAM - CURRENT

Well Name: Hartman 5
API # 04111-04441
Field: Ventura
Well Type: Producer
Drill Date: 10/20/1947
Sidetrack Date: 2/11/1949
KB: 9' above G.L. 508'

Base of Freshwater: 227'

Base of USDW: 1951'

Top of Hydrocarbon: 6835'

Barnard Fault Base: 7394'


AO-D: 8141'

T110 Fault Base: 9181'

H14 Fault Base: 10,095'

DC-H14: 10,715'

T180 Fault Base: 11,237'

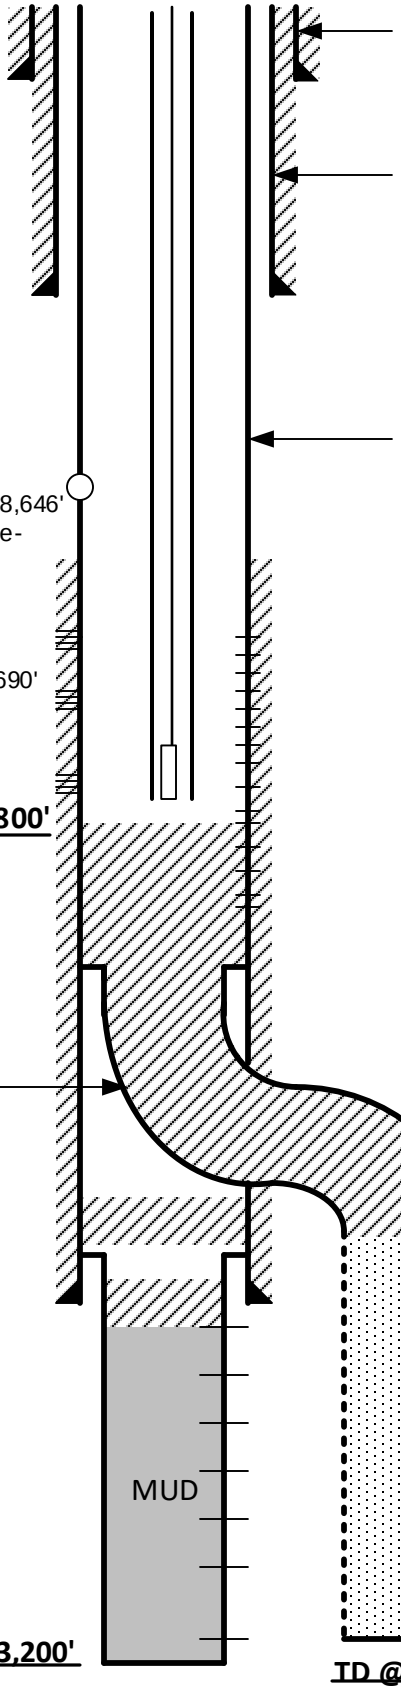

CASING DETAIL:
16" 62# H-40
0' - 116'
Cemented with 140 sx in 20" hole.
Cement to surface

CASING DETAIL:
11-3/4" 47# &54# J-55
0'-3658' (Total)
0' - 34' 54#
34'-2519' 47#
2519'-3658' 54#
Cemented w/ 1,000 sx from 3,658' and
500 sx from port @ 697' in 15" hole.
ETOC: Surface

CASING DETAIL:
7" 32# 35# 38# N-80
0' - 12,558' (Total)
0'-5' 32#
5'-45' 38#
45'-6429' 32#
6429'-8282' 35#
8282'-12,558' 38#
Cemented w/ 1,000 sx in 10-5/8" hole
ETOC: ~9147'

Squeezed casing hole @ 8,646'
w/ 180 sx of cement and re-
squeezed hole w/100 sx

WSO (4) 3/8"holes @
10,438', 11,610' and 11,690'
squeezed w/ cement

PBTD 11,800'

8/10/49: Plugged back w/ 180 sx
from 12,234' to 11,800'

7" PERF DETAILS:
10,440'- 11,680' (Total)
3-1/8"(4) SPF 90°phasing
10,440'- 11,184'
(2) 1/2" HPF
10,490' - 10,560', 10,950' - 10,985'
(2) 3/8" HPF
11,255' - 11,370', 11,530' - 11,575'
(2) HPF
11,615' - 11,680'

KOP:12,365'

LINER DETAIL:
5" 18# N-80
12,266' - 13,150' Slotted
Cmt'd thru perfs @ 12,709'
w/ 75 sx, re-cemented lap
w/ 85 sx

CLOSED PERFORATIONS:
15 gauge
12,711' - 13,150'
(4) 1/4" HPF
12,714' - 13, 064'

OH DETAILS:
TD: 13,200'
PBMD: Plugged back from 12,691'
to12,736' w/ 50 sx of cement.
Kick off plug from to
12,248' to 12,384'
KOP:12,365'
Abandoned Liner: 5" 18# N-80
12,444' - 13,195'
Perfs 12,715'-13,195'
Parted liner at 12,737'

CLOSED PERFORATIONS:
WSO Holes @
12,701', 12,702' and 12,703'
squeezed w/ cement

TD @ 13,200'

TD @ 13,155'
