
Wellname: HILL 641A API: 0403041634

3/21/2023

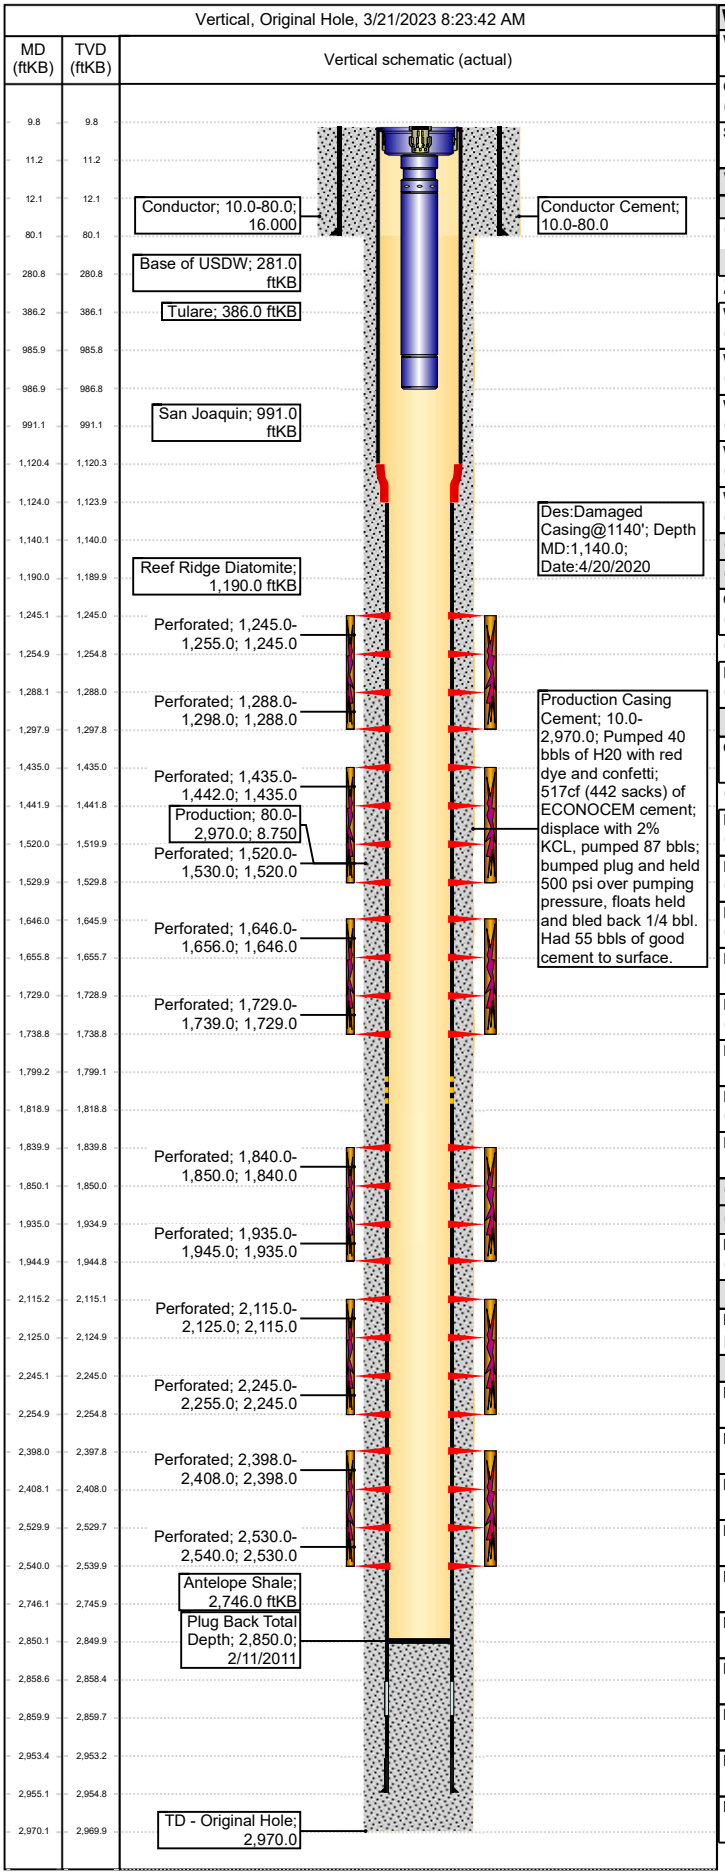

WELL INFORMATION

Well Name	Field Name	API/UWI (10)	Plug Back TD (ftKB)	TD (max)...
HILL 641A	SOUTH BELRIDGE	0403041634	Original Hole - 2,850.0	2,970.0

Ground Elevation (NAD 83) (ft)	KB-Ground Distance (ft)	Spud Date	Rig Release Date
604.70	10.00	12/5/2010	12/8/2010

Section	Township	Range	Meridian	Datum	Latitude (°)	Longitude (°)
19	28S	21E	MD	NAD 83	35.4828872700	-119.7539291400

WELLBORE SECTIONS

Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Conductor	16	10.0	80.0
Production	8 3/4	80.0	2,970.0

Zones

Wellbore	Zone Name	Top (ftKB)
Original Hole	Base of USDW	281.0
Original Hole	Tulare	386.0
Original Hole	San Joaquin	991.0
Original Hole	Reef Ridge Diatomite	1,190.0
Original Hole	Antelope Shale	2,746.0

CASING DATA

Conductor

Casing Description	Run Date	OD (in)	ID (in)	Grade	Wt/Len (lb/ft)	Top (ft...	Set Depth...
Conductor	12/5/2010	13 3/8	12.62	J-55	54.50	10.0	80.0

Casing Components

Item Description	OD (in)	ID (in)	Length (ft)	Wt (lb/ft)	Grade	Top (ftKB)	Btm (ftKB)
Conductor	13.375	12.615	70.00	54.50	J-55	10.0	80.0

Production

Casing Description	Run Date	OD (in)	ID (in)	Grade	Wt/Len (lb/ft)	Top (ft...	Set Depth...
Production	12/8/2010	7	6.37	J-55	23.00	0.0	2,955.0

Casing Components

Item Description	OD (in)	ID (in)	Length (ft)	Wt (lb/ft)	Grade	Top (ftKB)	Btm (ftKB)
Casing Joints	7.000	6.366	1,120.49	23.00	J-55	0.0	1,120.5
Cross Over	7.000	4.950	3.67	23.00	C-75	1,120.5	1,124.1
Casing Joints	5.500	4.950	675.17	15.50	J-55	1,124.1	1,799.3
Marker Joint	5.500	4.950	19.73	15.50	J-55	1,799.3	1,819.0
Casing Joints	5.500	4.950	1,039.65	15.50	J-55	1,819.0	2,858.7
Float Collar	5.500	4.950	1.19	15.50	J-55	2,858.7	2,859.9
Casing Joints	5.500	4.950	93.66	15.50	J-55	2,859.9	2,953.5
Float Shoe	5.500	4.950	1.48	15.50	J-55	2,953.5	2,955.0

CEMENT DATA

Conductor, 80.0ftKB


Description	Type	Top (ftKB)	Btm (ftKB)	Full R...	Vol Cement Ret (bbl)
Conductor Cement	Casing	10.0	80.0	No	0.0

Production, 2,955.0ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full R...	Vol Cement Ret (bbl)
Production Casing Cement	Casing	10.0	2,970.0	Yes	55.0

PERFORATION DATA

Date	Type	Top (ftKB)	Btm (ftKB)	Entere...	Est Hole...	Comment
1/31/2011	Perforated	1,245.0	1,255.0	10		Frac Stg 6
1/29/2011	Perforated	1,288.0	1,298.0	10		Frac Stg 6
1/31/2011	Perforated	1,435.0	1,442.0	7		Frac Stg 5
1/29/2011	Perforated	1,520.0	1,530.0	10		Frac Stg 5
1/30/2011	Perforated	1,646.0	1,656.0	10		Frac Stg 4
1/29/2011	Perforated	1,729.0	1,739.0	10		Frac Stg 4
1/30/2011	Perforated	1,840.0	1,850.0	10		Frac Stg 3
1/29/2011	Perforated	1,935.0	1,945.0	10		Frac Stg 3
1/30/2011	Perforated	2,115.0	2,125.0	10		Frac Stg 2
1/29/2011	Perforated	2,245.0	2,255.0	10		Frac Stg 2

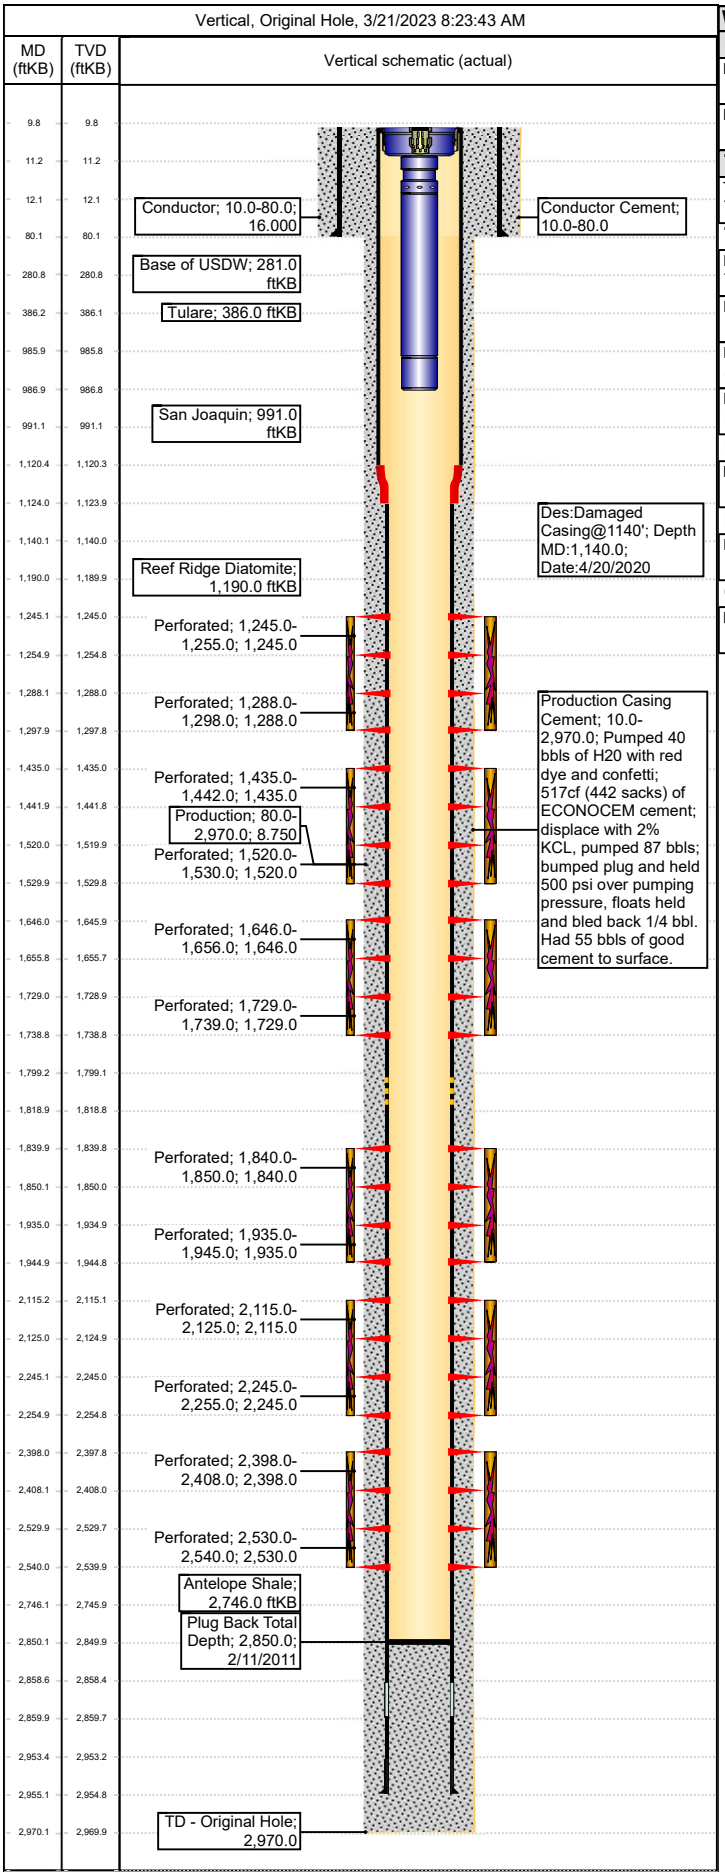

WELL INFORMATION

PERFORATION DATA

Date	Type	Top (ftKB)	Btm (ftKB)	Entere...	Est Hole...	Comment
1/29/2011	Perforated	2,398.0	2,408.0	10		Frac Stg 1
1/29/2011	Perforated	2,530.0	2,540.0	10		Frac Stg 1

TUBING DATA

Tubing Description	Set Depth (ft...	Run Date	Comment
Tubing - Production	987.0	4/21/2020	

Tubing Components

Item Description	OD (in)	ID (in)	Wt (lb/ft)	Joints	Length (ft)
Tubing Hanger	6.350			1	1.00
Fatigue Nipple	2.875	2.441		1	1.00
(31) 2 7/8 Tubing	2.875	2.441	6.50	31	974.00
BELL COLLAR	2.875	2.441		1	1.00

Rod Strings

Rod Description	Set Dept...	Run Date	Comment

Rod Components

Item Description	OD Nominal (in)	Joints	Length (ft)

Other In Hole

Description	Top (ftKB)	Btm (ftKB)	OD (in)	Comment
