Wellbore Schematic

Operator: Aera Energy LLC
Well: 948C-28
Type: Producer
Wellbore: 00
API : 0403033530

Datum: KELLY BUSHING @ 603.26ft (default)
Ground Elev: 591.26ft
PBMD: 2,143.17ft
TD MD: 2,174ft
Orientation: Directional
Spud / KO Date: 7/3/2007

CASING

Size(in)	Top MD(ft)	Base MD(ft)
14.0000	12.00	52.0
9.6250	13.00	202.0
7.0000	12.00	2,163.5

CEMENT STAGES

Job Type: Primary Date: 7/3/2007

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
9.6250	12.2500	13	202

Job Type: Primary Date: 7/23/2007

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	8.7500	12	2,164

REMARKS

Primary: 9.625" Surface Casing cemented at 202' to 13' with 86 sks of A-4 Versamix Surface CLASS C cement at 13.5 ppg, .25% BWOC FDP-C572, .6% BWOC VERSASET, 35% BWOC SILICA FLOUR, 37lbs/Sack POZMIX A, 5% BWOW SALT with yield of 1.74 cf/sk. 5 bbls of cement returns to surface.

Primary: 7" Production Casing cemented at 2163.53' to 12' with 168 sks of B-3 Slim Hole Design CLASS C cement at 12 ppg, 30% BWOC SILICA FLOUR with yield of 2.71 cf/sk. 4 bbls of cement returns to surface.

MARKER DETAILS

Name	MD top(ft)
Tulare	70.25
San Joaquin/Etchegoin	670.03
Reef Ridge Diatomite	710.00

PLUG DETAILS

Assembly name: TUBING

Type	Top MD(ft)	Btm MD(ft)
Tubing Hanger	12	13
Tubing Fatigue Nipple	13	14
X-Over	14	15
Pup Joint	15	29
Tubing	29	532
Tubing Drain	532	532
Tubing	532	597
Rod Pump Shoe	597	597
Chamfered Collar	597	598

Assembly name: ROD STRING

Type	Top MD(ft)	Btm MD(ft)
Polished Rod	12	42
Pony Rod(s)	42	58
SUCKER ROD(S)	58	538
Rod Shear Tool	538	538
SUCKER ROD(S)	538	598
Stabilizer Bar 4' w/3 guides	598	602
Rod Pump	602	618

ABANDONMENT


Abandonment Tag Depth:

BASE OF USDW

Base MD (ft) N/A

BASE OF FRESH WATER

Base MD (ft) N/A

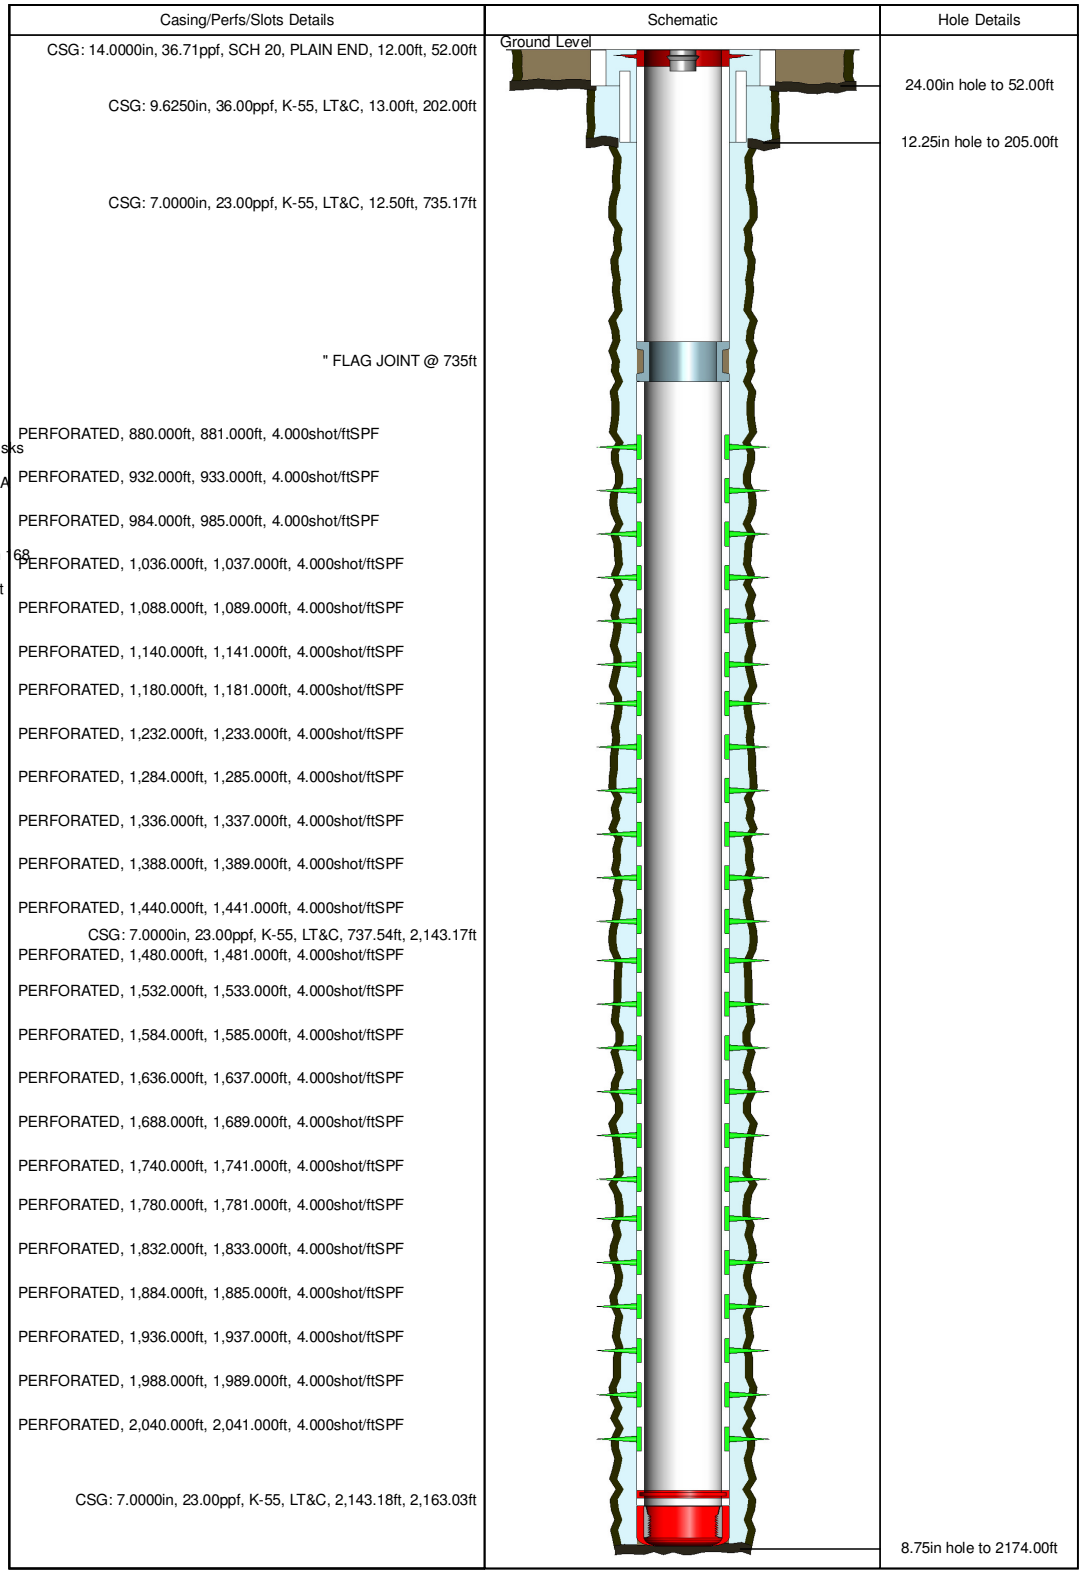

Obstruction Comments OD(in) Top MD(ft) Ba

Well Notes:

Initials: xyz Date: 11/30/2023
