OCCIDENTAL OF ELK HILLS INC


73SW-2G

Field Name: ELK HILLS
API-10: 0403035771
Spud Date: 5/13/2008
Site Name: 02G

Ground Level: 782.8ft Datum Elevation:
Original KB @ 796.80ft (default)

Wellbore: ORIGINAL HOLE
PBMD: 3,534.0ft
Btm TMD: 3,583.0ft
Btm TVD: 3,576.6ft
Btm Coordinates N/S: 2,284,836.04usft
Btm Coordinates E/W: 6,154,781.14usft

Schematic (6/10/2018)

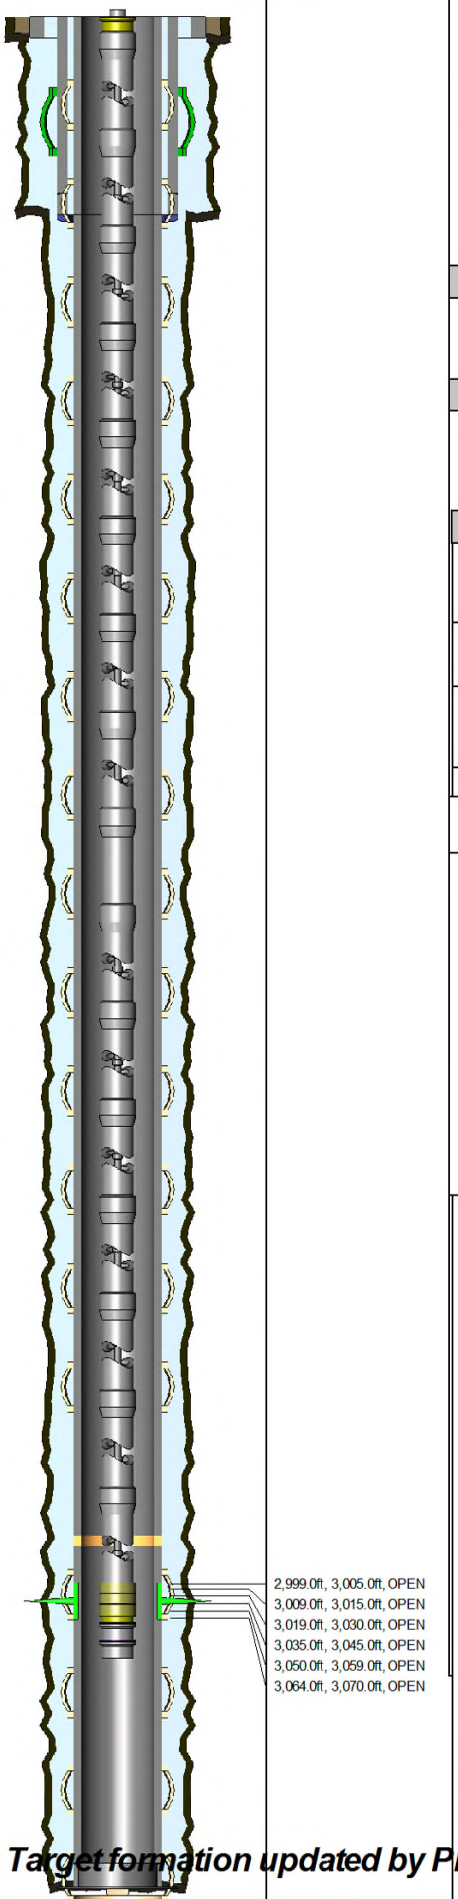

Opening Details

TUBING STRING — Report date: 6/9/2018

Component	Top MD(ft)	Btm MD(ft)	Nominal OD(in)	Weight(ppf)
TH-ROT	14.0	14.0	7.000	
FATNIP	14.0	14.7	2.875	
PUPJNT	14.7	41.3	2.875	6.50
CAS	41.3	2,999.6	2.875	6.50
BJ	2,999.6	3,019.0	2.875	
FATNIP	3,019.0	3,020.2	2.875	
BJ	3,020.2	3,039.6	2.875	
FATNIP	3,039.6	3,040.7	2.875	
BJ	3,040.7	3,059.6	2.875	
PUPJNT	3,059.6	3,075.6	2.875	6.50
STNIP	3,075.6	3,076.7	2.875	
CAS	3,076.7	3,108.0	2.875	
DESAND	3,108.0	3,111.0	2.875	
TBGJNT	3,111.0	3,142.6	2.875	

PLUG BACK — Report date: 5/18/2008

Component	Top MD(ft)	Btm MD(ft)	Nominal OD(in)	Weight(ppf)
CEMENT	3,534.0	3,580.0	6.366	
CEMENT	3,580.0	3,583.0	9.500	

ROD STRING — Report date: 6/10/2018

Component	Top MD(ft)	Btm MD(ft)	Nominal OD(in)	Weight(ppf)
POLROD	0.0	30.0	1.250	
PNYROD	30.0	42.0	0.750	
ROD	42.0	3,072.0	0.750	
STB3P	3,072.0	3,076.0	0.875	

CONDUCTOR CASING — Report date: 5/9/2008

Component Name	Top MD(ft)	Btm MD(ft)	Nominal OD(in)	Weight(ppf)	Grade
CASING JOINT(S)	14.0	54.0	14.000		

SURFACE CASING — Report date: 5/13/2008

Component Name	Top MD(ft)	Btm MD(ft)	Nominal OD(in)	Weight(ppf)	Grade
CASING JOINT(S)	14.0	350.7	9.625	36.00	J-55
INSERT FLOAT	350.7	350.7	9.625	36.00	J-55
CASING JOINT(S)	350.7	390.0	9.625	36.00	J-55
CASING SHOE	390.0	391.0	9.625	36.00	J-55

PRODUCTION CASING — Report date: 5/18/2008

Component Name	Top MD(ft)	Btm MD(ft)	Nominal OD(in)	Weight(ppf)	Grade
CASING JOINT(S)	14.0	2,909.4	7.000	23.00	K-55
FLAG JOINT	2,909.4	2,929.1	7.000	23.00	K-55
CASING JOINT(S)	2,929.1	3,534.2	7.000	23.00	K-55
FLOAT COLLAR	3,534.2	3,535.4	7.000		
CASING JOINT(S)	3,535.4	3,579.1	7.000	23.00	K-55
GUIDE SHOE	3,579.1	3,580.0	7.000		

Hole Sections	Top MD(ft)	Base MD(ft)
16" HOLE	14.0	54.0
13.5" HOLE	54.0	391.0
9.5" HOLE	391.0	3,583.0

TTOC

Job Type: Primary
Report date: 5/13/2008
TOC locate method: Cmt Returns at Surf
Drilled out date:

Assembly Size	Top MD(ft)	Btm MD(ft)	Returns	Est Cmt Vol Returns to Surf(bbl)
9.625	14.0	391.0	Full	20.0

Job Type: Primary
Report date: 5/18/2008
TOC locate method: Cmt Returns at Surf
Drilled out date:

Assembly Size	Top MD(ft)	Btm MD(ft)	Returns	Est Cmt Vol Returns to Surf(bbl)

Start Date: 5/28/2008 00:00 Contractor: HALLIBURTON
Conveyed: WIRELINE

Date Shot	Top MD(ft)	Bottom MD(ft)	Shot Diam.(in)	Density(shot/ft)	Phasing(°)
5/28/2008	2,999.0	3,005.0	0.370	5.00	60.00
5/28/2008	3,009.0	3,015.0	0.370	5.00	60.00
5/28/2008	3,019.0	3,030.0	0.370	5.00	60.00
5/28/2008	3,035.0	3,045.0	0.370	5.00	60.00
5/28/2008	3,050.0	3,059.0	0.370	5.00	60.00
5/28/2008	3,064.0	3,070.0	0.370	5.00	60.00

y: Target formation updated by PIT team DOGGR_FIELD_NAME updated by CRC Universe team Target formatio
