Wellbore Schematic

Operator: Aera Energy LLC
Well: 943RR-29
Type: Producer
Wellbore: 00
API no.: 0403058245

Datum: KELLY BUSHING @ 627.61ft (default)
Ground Elev: 612.61ft
PBMD: 1,902.58ft
TD MD: 1,933ft
Orientation: Directional
Completion Date: 12/29/2015

CASING

Size(in)	Top MD(ft)	Base MD(ft)
14.0000	15	55
9.6250	15	407
7.0000	15	1,923

CEMENT STAGES

Job Type: Primary Date: 12/4/2015

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
9.6250	12.2500	15	407

Job Type: Primary Date: 12/9/2015

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
7.0000	8.7500	15	1,923

REMARKS

SURFACE CASING Cement Report:
Ran 9.625", 36#, K-55, LTC, to 407.2' MD Pumped 301 ft³ (53.6 bbls) 146 sks of LEAD A-5 SwiftCem TYPE III cement at 14 ppg, 35% Silica Flour, 4% CaCl2, with yield of 2.06 ft/sk. CIP on 12/4/2015 12:01:00 AM. 20 bbls of cement to surface.

PRODUCTION CASING Cement Report:
Ran 7", 23#, K-55, BT&C, to 1922.96' MD Pumped 449 ft³ (80 bbls) 174.8 sks of LEAD B-3 EconoCem TYPE III cement at 12 ppg, 30% Silica Flour, ¼#/Flocele, with yield of 2.57 ft/sk. CIP on 12/9/2015 1:30:00 AM. Bumped plug. Floats held. 13 bbls of cement to surface.

MARKER DETAILS


Name	MD top(ft)
Tulare	154.42
San Joaquin/Etchegoin	735.16
Reef Ridge Diatomite	785.00

PLUG DETAILS

Assembly name: TUBING

Type	Top MD(ft)	Btm MD(ft)
Tubing Hanger	15	16
Tubing Fatigue Nipple	16	16
	16	17
Tubing	17	800
	800	800

Initials: AW Date: 5/16/2022

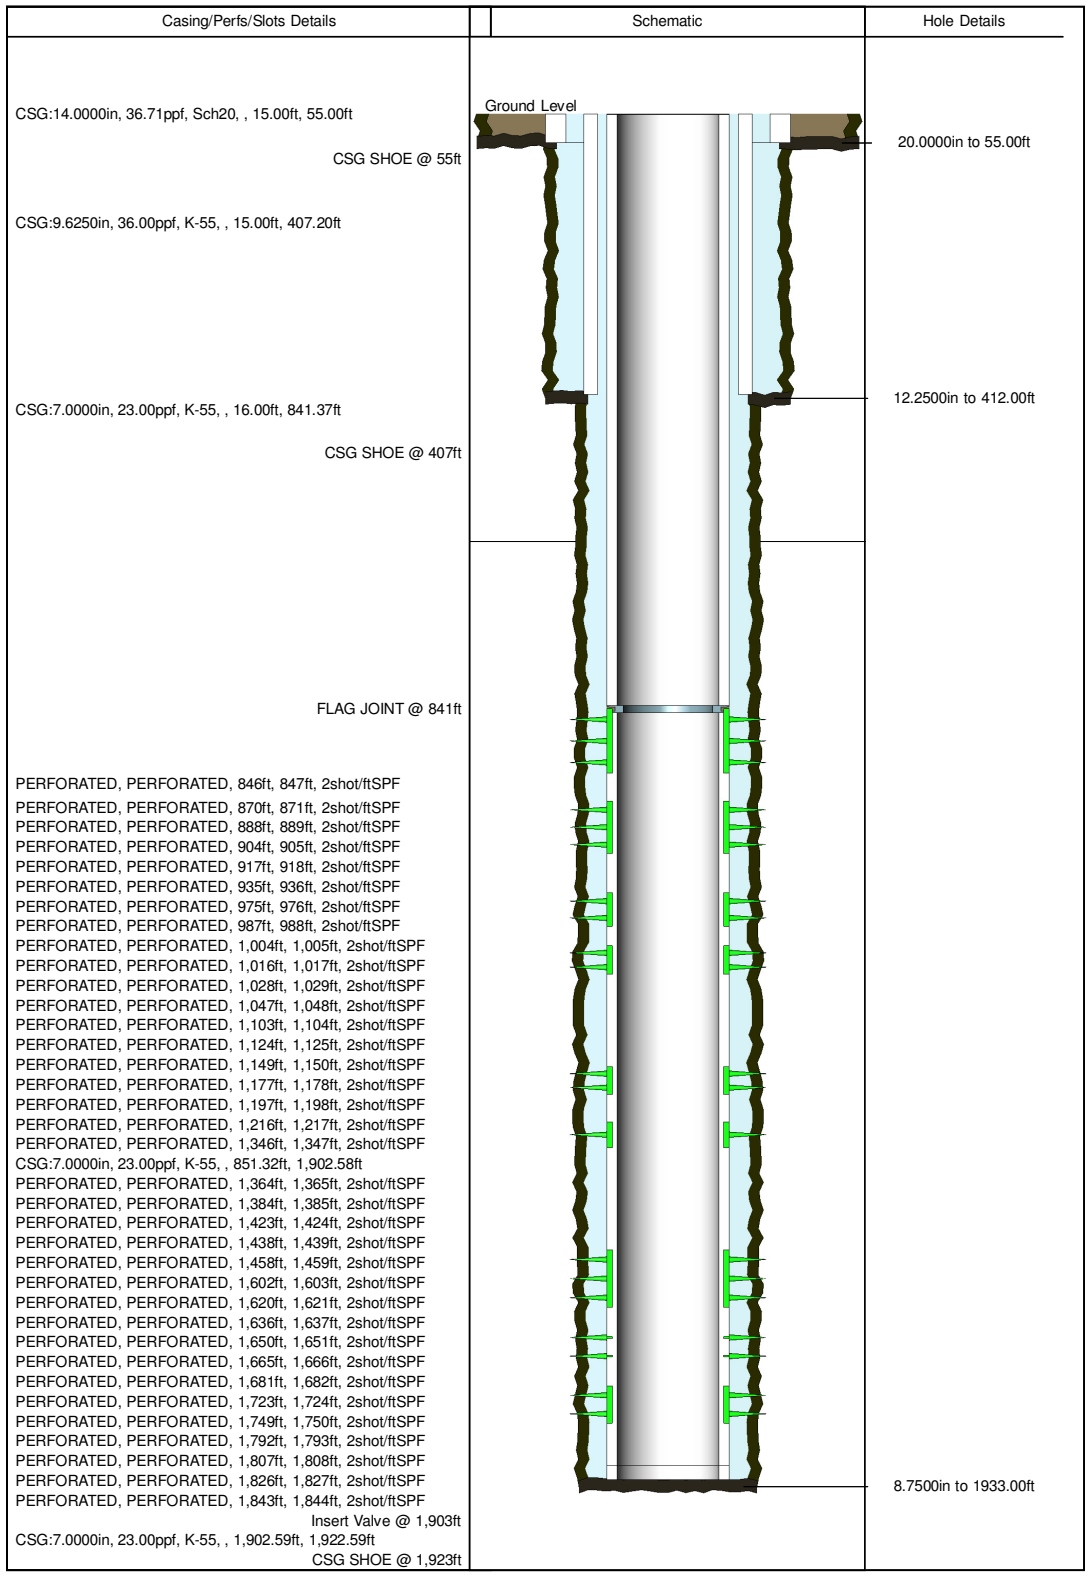

Well Notes:
