Well
Hartman East 47

API #: 04-111-04666-00
Sec 22, T3N, R23W

Unless otherwise noted, cmt yield is estimated to be 1.16

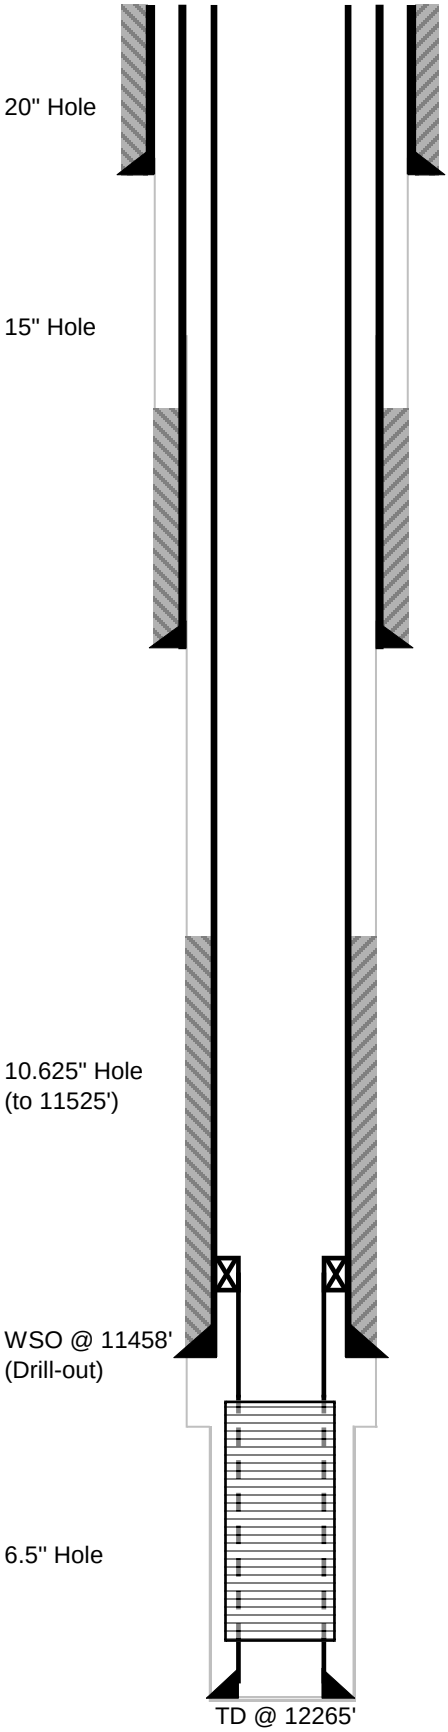

16" ETOC @ Surface

16", 63#, B CSG @ 378'
CMT'D w/ 350 SKS CMT, all treated

11.75" ETOC @ 3791'

11.75", 54#/60#, J-55 CSG @ 5200'
CMT'D w/ 600 SKS Colton Slow CMT

7.625" ETOC @ 7737'

Top of 5" Liner @ 11416'

7.625", 29.7#/33.7#/39#, N-80 CSG @ 11458'
CMT'D w/ 1000 SKS Colton Hi-Temp CMT

5" Perfs: 0.25", (108) HPF w/ 12M Wire Wrapped Screen @ 11481-12241'

5", 18#, N-80 Liner @ 12265'

Operator: Aera Energy LLC
Lease: Hartman East
Well Type: Producer
Status: Operational
Flood: DN
Base of Fresh Water: No
Directional: Yes

GL Elevation: 567.8' asl (See Notes)
Datum to GL: 10' KB (See Notes)

Drill Date: 7/4/1954

Junk: None

Notes

Lost circulation while drilling 10.625" Hole @ 5581-5614'. CMT'D w/ 800 SKS total, drilled out 441 LF CMT total, regained circulation @ 5614'

Cut down rig site 17' & repaired same. Revised elevation is 550.62' asl. (7/1973)

Top of Zone Markers

Za-C	4665'	DF-D	9014'
AC-C	4997'	DH-D	9129'
AE1-C	5233'	DL-D	9212'
AG-C	5432'	DO-D	9358'
AH-C	5578'	DP-D	9455'
AK-C	5745'	DR-D	9545'
AM-C	6020'	DS-D	9600'
AO-C	6236'	DR-T110	9705'
AP-C	6384'	FB-T110	9915'
AQ1-C	6588'	FC-T110	10017'
AR-C	6732'	FF-T110	10058'
AS-C	6840'	FH-T110	10237'
AT-C	7200'	FJ-T110	10324'
AP-D	7587'	FK-T110	10440'
AQ-D	7725'	FL-T110	10484'
AQ1-D	7766'	FM-T110	10595'
AR-D	7888'	FO-T110	10674'
AS-D	7948'	FP-T110	10727'
AT-D	8140'	FQ-T110	10777'
AU-D	8260'	FR-H14	11105'
AU1-D	8395'	FS-H14	11134'
AV-D	8502'	FT-H14	11218'
AW-D	8648'	HA-H14	11270'
AW2-D	8670'	HF-H14	11354'
AX-D	8700'	HG-H14	11424'
DA-D	8793'	HK-H14	11825'
DC-D	8859'	HL1-H14	12101'
DD-D	8936'		
DE-D	9000'		

Prepared by: LTH (11/6/2013)
Updated by: J. Kahler (05/10/2016)

InterAct
