Operator: Aera Energy LLC
Well: MCG021
Type: Injector
Wellbore: 07
API : 0411104888

Wellbore Schematic

Datum: KELLY BUSHING @ 598.21ft (default)
Ground Elev: 575.21ft
PBMD: 10,433ft
TD MD: 10,435ft
Orientation: Directional
Spud / KO Date: 6/20/1984

CASING

Size(in)	Top MD(ft)	Base MD(ft)
20.0000	23	120.0
13.3750	23	695.0
9.6250	23	6,118.0
6.6250	5,730	10,433.0

CEMENT STAGES

Job Type: Primary Date: 7/14/1984

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
6.6250	8.5000	5,730	10,433

Job Type: Squeeze Date: 9/1/1984

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
6.6250	8.5000	9,986	9,987
6.6250	8.5000	9,629	9,630

Job Type: Primary Date: 2/5/1945

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
13.3750	17.0000	23	695

Job Type: Primary Date: 3/9/1945

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)
9.6250	12.2500	4,221	6,118

REMARKS

Primary: 6.625" casing cemented at 10433' to 5730' with 422 sks of Unknown CLASS G cement at 10.6 ppg, with yield of 2.45 cf/sk. Followed by 161 sks of Unknown CLASS G cement at 15.3 ppg, with yield of 1.24 cf/sk. Good cement returns to TOL at 5730'.

Squeeze: 6.625" squeezed at 9630' to 9629' with 13 sks of Unknown CLASS G cement at 15.8 ppg, with yield of 1.15 cf/sk.
Squeeze: 6.625" squeezed at 9987' to 9986' with 14 sks of Unknown CLASS G cement at 15.8 ppg, with yield of 1.15 cf/sk.

Primary: 13.375" casing cemented at 695' to 23' with 450 sks of Unknown cement at 16.2 ppg, with yield of 1.08 cf/sk. Good cement returns to surface.

Primary: 9.625" casing cemented at 6118' to 4221' with 550 sks of Unknown cement at 16.2 ppg, with yield of 1.08 cf/sk. Cement returns to surface not stated. ETOC at 4221'.

PLUG DETAILS

Type	Top MD(ft)	Btm MD(ft)

ABANDONMENT

Abandonment Tag Depth: N/A

UIC Project Code(s)

UIC: 8140011 - D-6

BASE OF USDW

Base MD (ft) 1260

BASE OF FRESH WATER

Base MD (ft) N/A


PERFORATIONS

Top MD(ft)	Bottom MD(ft)	Density(shot/ft)
8,970.00	9,096.00	4.00
9,107.00	9,220.00	4.00
9,237.00	9,390.00	4.00
9,537.00	9,613.00	4.00
9,629.00	9,630.00	4.00
9,656.00	9,692.00	4.00
9,708.00	9,714.00	4.00
9,718.00	9,733.00	4.00
9,743.00	9,750.00	4.00
9,778.00	9,857.00	4.00
9,946.00	9,975.00	4.00
9,986.00	9,987.00	4.00
10,013.00	10,133.00	4.00
10,140.00	10,200.00	4.00
10,240.00	10,299.00	4.00

MARKER DETAILS

Name	MD top(ft)
A-1	935.00
EST Base of <10000ppm	1,259.63
A-2	3,256.00
C-1	3,829.00
C-2	4,379.00
C-3	5,690.00
C-4	6,992.52
C-5	7,958.00
D-3	8,107.00
D-4	8,280.00
D-5	8,865.00
D-6	9,647.00
D-7	10,300.00

Casing/Slots Details
CSG: 20.0000in, 94.00ppf, H-40, , 23.00ft, 120.00ft
CSG: 13.3750in, 48.00ppf, H-40, , 23.00ft, 695.00ft
CSG: 9.6250in, 40.00ppf, J-55, , 23.00ft, 1,901.00ft
CSG: 9.6250in, 43.50ppf, J-55, , 1,901.00ft, 2,713.00ft
CSG: 9.6250in, 40.00ppf, N-80, , 2,713.00ft, 4,282.00ft
CSG: 9.6250in, 43.50ppf, N-80, , 4,282.00ft, 5,930.00ft
CSG: 9.6250in, 43.50ppf, N-80, , 5,930.00ft, 5,932.00ft
CSG: 6.6250in, 24.00ppf, , , 5,730.00ft, 9,565.00ft
CSG: 6.6250in, 28.00ppf, , , 9,565.00ft, 10,433.00ft

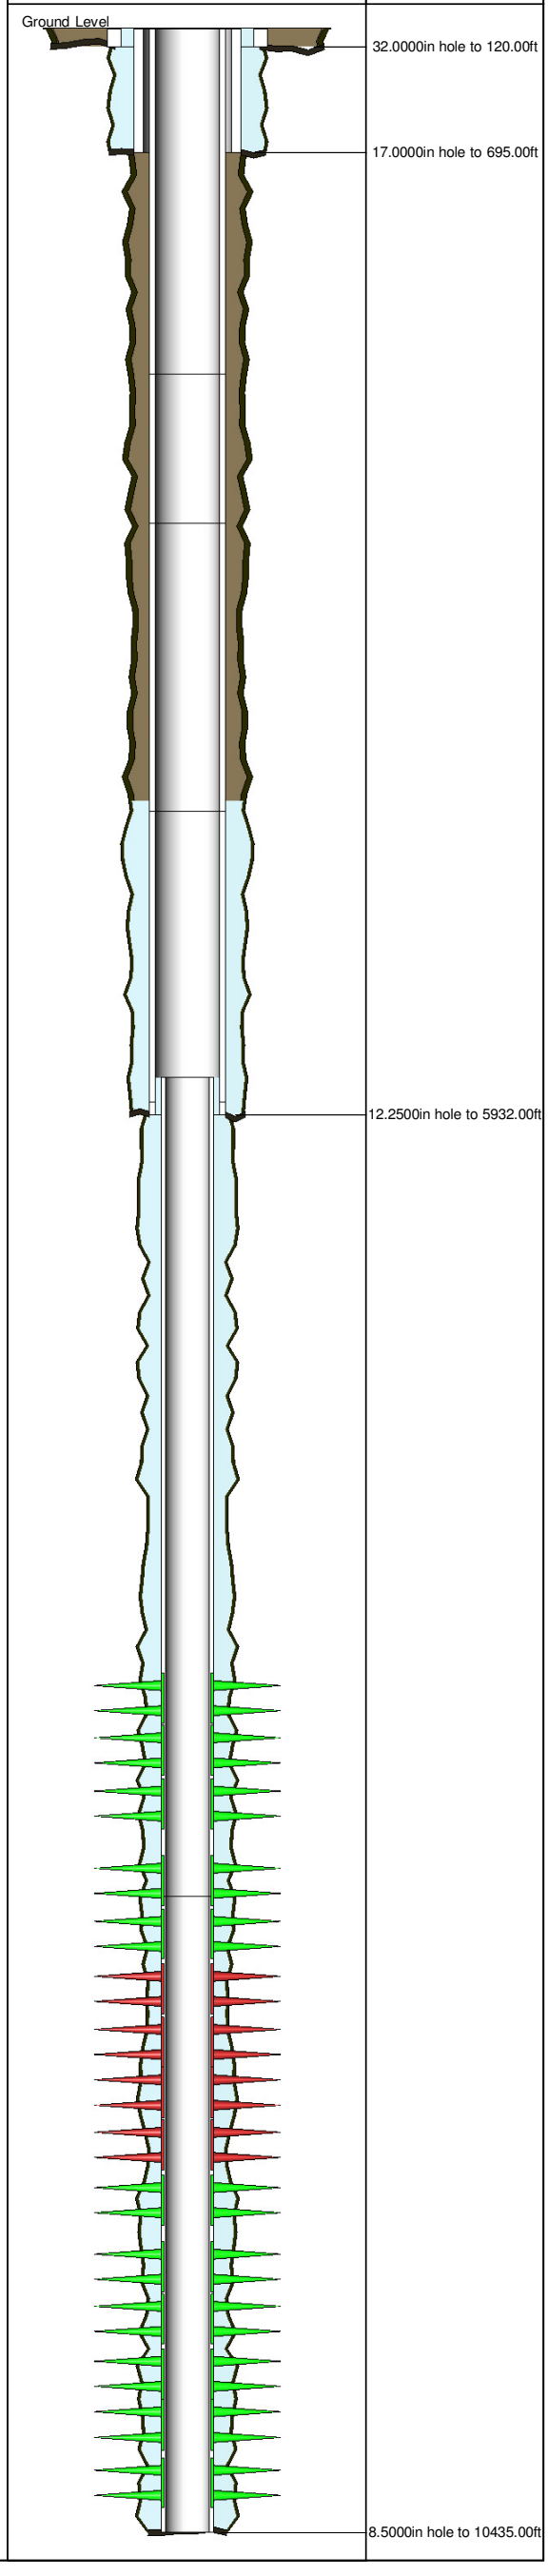

Hole Details
32.0000in hole to 120.00ft
17.0000in hole to 695.00ft
12.2500in hole to 5932.00ft
8.5000in hole to 10435.00ft

Obstruction	Comments	OD(in)	Top MD(ft)	Base MD(ft)
DAMAGED CSG.	Holes found @ 1911' with 9 - 5/8" 43# fullbore.	9.6250	1,911.00	
OBSTRUCTION	tight spot at 9588'.	6.6250	9,588.00	9,698.00

Well Notes:
Perforations at 9750' to 9656' were closed after holes found at 1911' were cemented on 10/20/1987. The cement was drilled out to 9900', where a 6.625" 28# bridge plug had been set on 10/15/1987. On 10/22/1987, after cement was drilled out, the bridge plug was retrieved.

Initials: MV239032 Date: 11/5/2021
