Well Name: RBH2 Wellbore Number: 01

Casing:
18.625" 88.2# 0ft - 643ft

ETOC @ Surface
Cmt'd w/925 sx (type cmt not found)
25" hole

Casing:
11" 54# 0ft - 3674ft
WSO
ETOC @ 2830''
Cmt'd w/500 sx Santa Cruz cmt, last 150 sx treated.
17" hole


Casing:
8.625" 40# 0ft - 4502ft
Milled window for R#1 3700-3745'

ETOC @ 1839'
Cmt'd w/425 sx Santa Cruz cmt, last 125 sx treated, from csg bottom @ 4502' in OH.
10-3/8" hole

Casing:
5.5" 17# 0ft - 4870ft
5.5" 15.5# 4870ft - 7484ft

ETOC @ 3774'
Cmt'd w/334 sx thru holes @ 4798'
7-5/8" hole

Shot 4 holes @ 7454'. Pumped 234 sx cmt 1:1 Di-Mix, 4% gel, followed by 100 sx Grade "G" cmt. Located cmt @ 5945' (drilled out to 6700'). Ran Cmt Bond Log & found cmt on outside of csg @ 3774'.

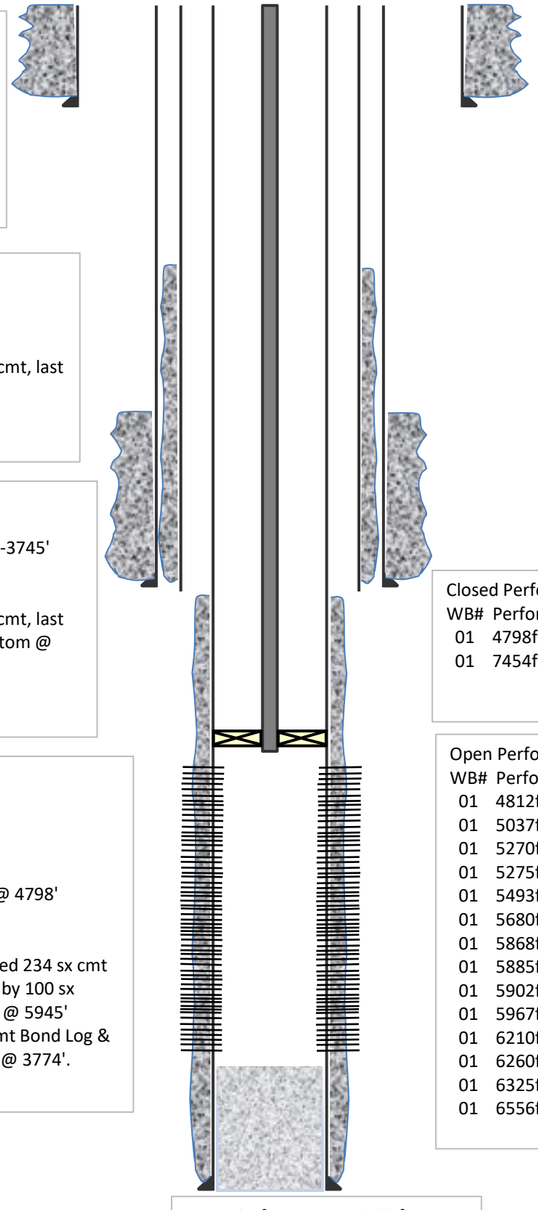

Closed Perforations:


WB#	Perforations	Description
01	4798ft - 4799ft	WSO-sqz w/50 sx LWL cmt
01	7454ft - 7455ft	WSO

Open Perforations:

WB#	Perforations	Description
01	4812ft - 4980ft	PERFORATED
01	5037ft - 5245ft	PERFORATED
01	5270ft - 5271ft	WSO
01	5275ft - 5432ft	PERFORATED
01	5493ft - 5630ft	PERFORATED
01	5680ft - 5800ft	PERFORATED
01	5868ft - 5869ft	WSO
01	5885ft - 5897ft	PERFORATED
01	5902ft - 5920ft	PERFORATED
01	5967ft - 6155ft	PERFORATED
01	6210ft - 6240ft	PERFORATED
01	6260ft - 6300ft	PERFORATED
01	6325ft - 6368ft	PERFORATED
01	6556ft - 6619ft	PERFORATED

TD: 7485 ft PBTD: 6700 ft

Geological Markers

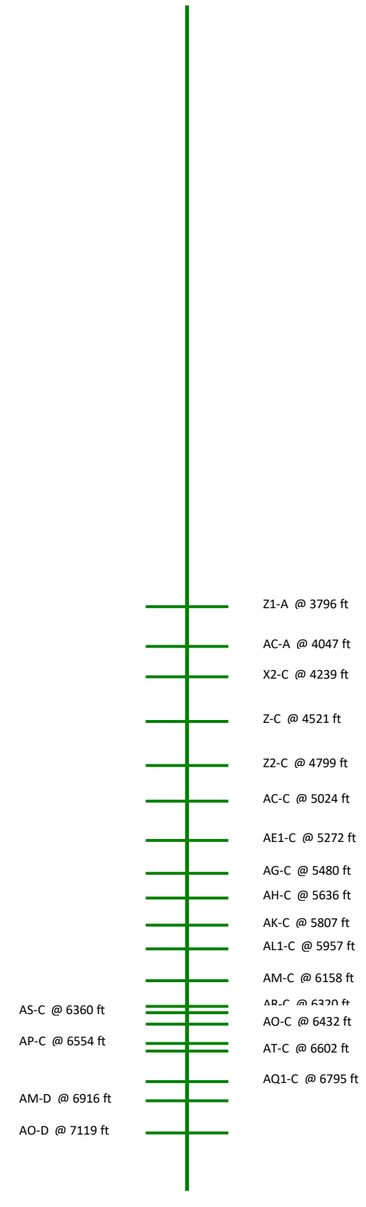

OPERATOR: Aera Energy LLC API NUMBER: 0411103998
WELLNAME: RBU L. HARTMANN 2 WELL TYPE: Injector
LEASE: HARTMANN SEC 21 T3N R23W
DIRECTIONAL: Deviated R#1 DRILL DATE: 08/03/1973
STATUS: OPERATIONAL R#1 KOP: 3700'
GL: 193' DATUM TO GL: 17.19' KB
BFW: Yes - 100 - 2M# FLOOD: RBU
DATE DRAWN: 12/21/2012 DRAWN BY: D. Drennan
DATE UPDATED: 05/12/2016 BY: D. DRennan

PLUGS / FILLS:
6700 ft to 7485 ft CEMENT PLUG Pumped 234 sx cmt 1:1 Di-Mix, 4% gel, followed by 100 sx Grade "G" cmt. Located cmt @ 5945' (drilled out to 6700').

TUBING DETAILS: As of 09/05/2005

Size	Weight	Grade	Thread	To From	Description
2.875''				12 ft - 13 ft	Tubing Fatigue Nipple
2.875''	6.5#	N-80	8rd	13 ft - 19 ft	Tubing Sub
2.875''				19 ft - 20 ft	Tubing Cross-over Joint
2.875''	6.5#	J-55	MAXTHRD	20 ft - 4671 ft	Tubing - 2 7/8"
2.875''				4672 ft - 4675 ft	Packer
2.375''				4675 ft - 4675 ft	Seating Nipple
2.375''				4676 ft - 4678 ft	Tubing Cross-over Joint
2.875''	6.5#	J-55	MAXTHRD	4678 ft - 4709 ft	Tubing - 2 7/8"
2.875''				4709 ft - 4709 ft	Tubing Fatigue Nipple

ENGINEERING NOTES:

Unless otherwise noted, Cmt yield is Estimated to be 1.16

JUNK LEFT IN HOLE FROM OO WELLBORE:
8-5/8" 40# csg @ 4400', sidetracked @ 3745'
5-3/16" 20# liner 4000-6592', perfs 4150-4290', 4832-6592', open hole 6592-7301'.

03/17/2003 CLEANOUT NOTES Tag fill @6374' unable to get deeper.

09/26/2005 CLEANOUT NOTES The rig had PU @ 5040', fell thru after 4' & tagged @ 5842'. C/O to 6469'.

09/27/2005 TIGHT SPOT Tight Spots @ 4920, 4980, 5030, 5040, 5666, & 5702'.

07/16/2015 MIT Passed MIT Test
08/19/2014 SAPT Passed SAPT Test

Wellsketch Version 4.3 - 12/03/2012
