Operator: Aera Energy LLC
Well: TAY420
Type: Injector
Wellbore: 01
API : 0411105257

Wellbore Schematic

Datum: DERRICK FLOOR @ 554.80ft (default)
Ground Elev: 543.80ft
PBMD: 13,003ft
TD MD: 13,580ft
Orientation: Vertical
Spud / KO Date: 10/24/1957

CASING

Size(in)	Top MD(ft)	Base MD(ft)
7.0000	11	12,264.0
5.0000	12,053	13,069.0
4.5000	13,069	13,563.0

CEMENT STAGES

Csg Size	Hole Size(in)	Top MD(ft)	Btm MD(ft)

REMARKS

UIC Project Code(s)

UIC:	N/A
UIC:	N/A
UIC:	N/A
UIC:	N/A

BASE OF USDW

Base MD (ft) 1657

BASE OF FRESH WATER

Base MD (ft) N/A

PERFORATIONS

Top MD(ft)	Bottom MD(ft)	Density(shot/ft)
11,212.00	11,222.00	1.00
11,237.00	11,247.00	1.00
11,263.00	11,393.00	4.00
11,462.00	11,477.00	4.00
11,513.00	11,524.00	4.00
11,531.00	11,541.00	4.00
11,548.00	11,554.00	4.00
11,569.00	11,599.00	4.00
11,623.00	11,653.00	4.00
11,672.00	11,677.00	4.00
11,685.00	11,690.00	4.00
11,703.00	11,726.00	4.00
11,774.00	11,779.00	4.00
11,894.00	11,904.00	2.00
11,965.00	11,995.00	4.00
12,030.00	12,040.00	4.00
12,236.00	12,320.00	2.00
12,334.00	12,345.00	2.00
12,378.00	12,392.00	2.00
12,412.00	12,436.00	2.00
12,446.00	12,542.00	2.00
12,578.00	12,614.00	2.00
12,620.00	12,646.00	2.00
12,654.00	12,738.00	2.00
12,764.00	12,888.00	2.00
12,894.00	12,906.00	2.00
12,919.00	12,933.00	2.00
12,938.00	12,978.00	2.00
13,002.00	13,003.00	4.00
13,035.00	13,036.00	4.00
13,037.00	13,038.00	4.00
13,040.00	13,041.00	4.00
13,070.00	13,170.00	4.00
13,180.00	13,280.00	4.00
13,290.00	13,360.00	4.00

Tubing	11,112	11,176
Pup Joint	11,176	11,178
X-Over	11,178	11,179
Ball Shear Sub	11,179	11,179

Assembly name: Bridge Plug

Type	Top MD(ft)	Btm MD(ft)
Bridge Plug	13,003	13,004

Assembly name: Other Plug

Type	Top MD(ft)	Btm MD(ft)
OTHER PLUG	13,563	13,580

MARKER DETAILS

Name	MD top(ft)
EST Base of <10000ppm	1,566.73
A-1	1,841.00
A-2	4,600.00
B-2	5,445.00
B-3	6,285.00
T410-4	8,812.00

ABANDONMENT

Abandonment Tag Depth: N/A

Casing/Slots Details	Equip. Details	Schematic	Hole Details

CSG: 7.0000in, 29.00ppf, S-95, ST&C, 11.00ft, 7,888.00ft

CSG: 7.0000in, 32.00ppf, N-80, , 7,888.00ft, 12,126.00ft

PERFORATED, 11,212.00ft, 11,222.00ft
PERFORATED, 11,237.00ft, 11,247.00ft
PERFORATED, 11,263.00ft, 11,393.00ft
PERFORATED, 11,462.00ft, 11,477.00ft
PERFORATED, 11,513.00ft, 11,524.00ft
PERFORATED, 11,531.00ft, 11,541.00ft
PERFORATED, 11,548.00ft, 11,554.00ft
PERFORATED, 11,569.00ft, 11,599.00ft
PERFORATED, 11,623.00ft, 11,653.00ft
PERFORATED, 11,672.00ft, 11,677.00ft
PERFORATED, 11,685.00ft, 11,690.00ft
PERFORATED, 11,703.00ft, 11,726.00ft
PERFORATED, 11,774.00ft, 11,779.00ft
PERFORATED, 11,894.00ft, 11,904.00ft
PERFORATED, 11,965.00ft, 11,995.00ft
PERFORATED, 12,030.00ft, 12,040.00ft
PERFORATED, 12,236.00ft, 12,320.00ft
PERFORATED, 12,334.00ft, 12,345.00ft
PERFORATED, 12,378.00ft, 12,392.00ft
PERFORATED, 12,412.00ft, 12,436.00ft
PERFORATED, 12,446.00ft, 12,542.00ft
PERFORATED, 12,578.00ft, 12,614.00ft
PERFORATED, 12,620.00ft, 12,646.00ft
PERFORATED, 12,654.00ft, 12,738.00ft

CSG: 5.0000in, 18.00ppf, N-80, X-LINE, 12,053.00ft, 13,060.00ft


PERFORATED, 12,764.00ft, 12,888.00ft
PERFORATED, 12,894.00ft, 12,906.00ft
PERFORATED, 12,919.00ft, 12,933.00ft
PERFORATED, 12,938.00ft, 12,978.00ft
PERFORATED, 13,002.00ft, 13,003.00ft

BP 5 in,, 13,003ft

PERFORATED, 13,035.00ft, 13,036.00ft
PERFORATED, 13,037.00ft, 13,038.00ft
PERFORATED, 13,040.00ft, 13,041.00ft

Slot Info: 0.3750, , 1.0000

PERFORATED, 13,070.00ft, 13,170.00ft
PERFORATED, 13,180.00ft, 13,280.00ft
SLOTTED, 13,069.00ft, 13,563.00ft
PERFORATED, 13,290.00ft, 13,360.00ft

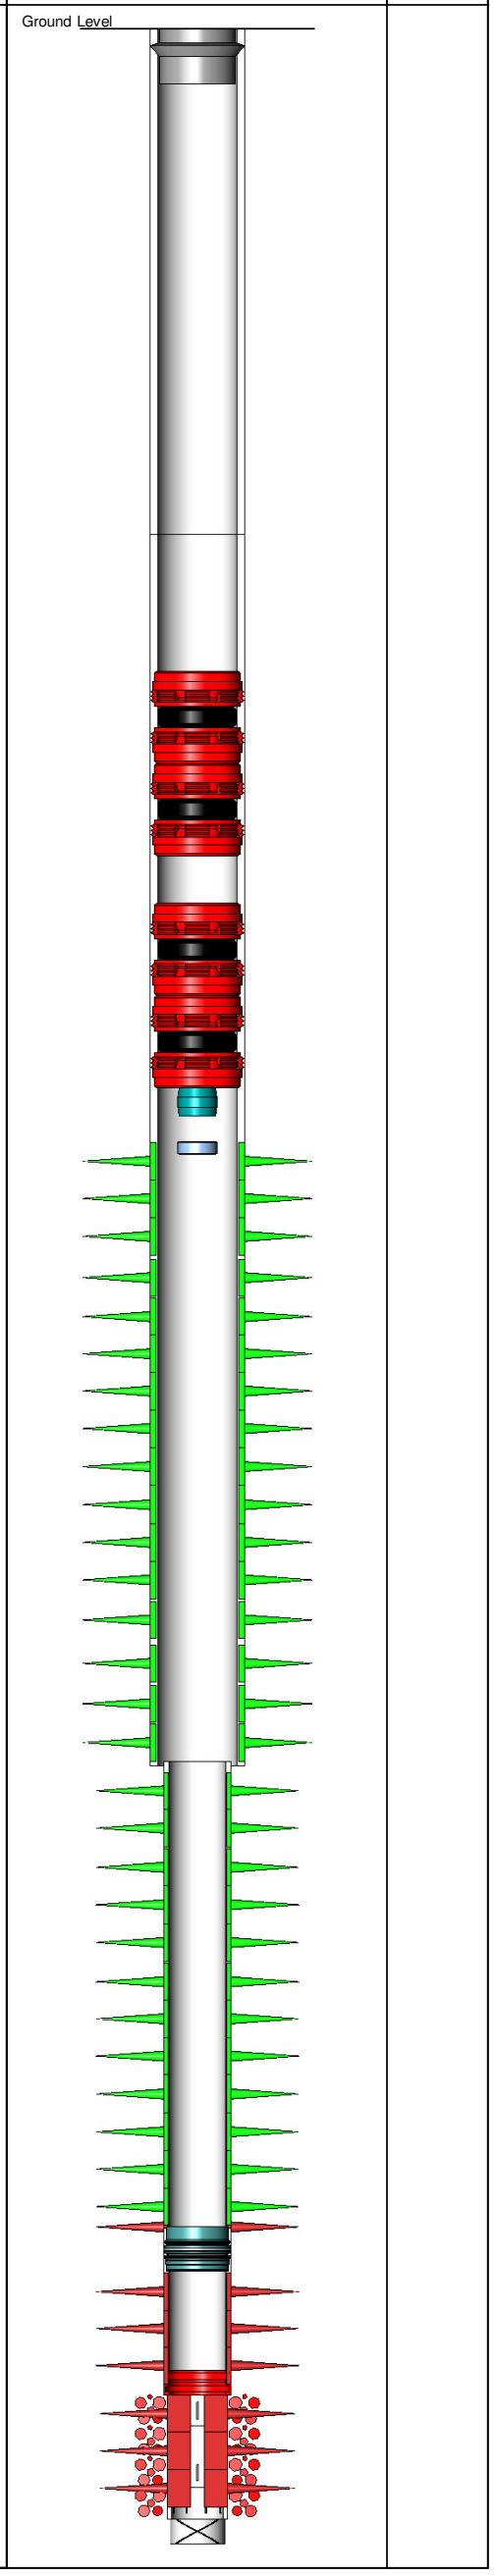

Obstruction Comments OD(in) Top MD(ft) Base MD(ft)

Well Notes:

Initials: xyz Date: 4/25/2022
