
Well
Lloyd Corp. 75 RD

API #: 04-111-04246-01
Sec 19, T3N, R22W

Unless otherwise noted, cmt yield is estimated to be 1.16

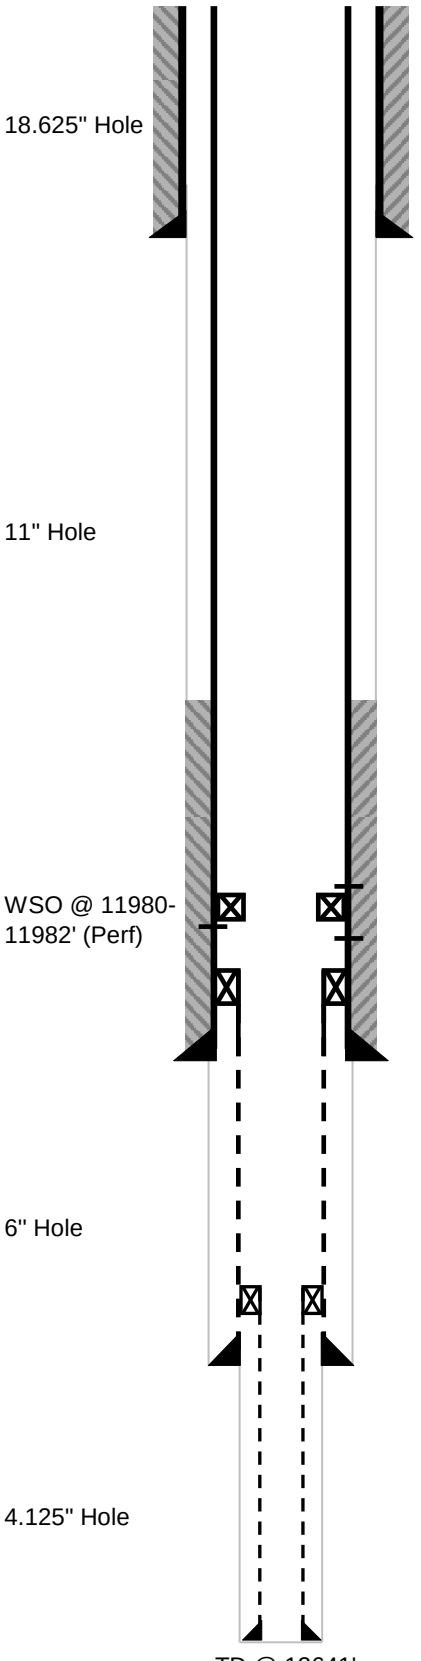

13.375" ETOC @ Surface

13.375", 48#/54.5#, J-55/H-40 CSG @ 838'
CMT'D w/ 825 SKS VCC CMT

7" ETOC @ 8549'

RD KOP (from OH) @ 9290' into this wellbore
(See History)

Eight (8) 0.5" Holes @ 11950-11952' (SQZ'D Away 28 SKS)
Junk @ 11963'
Eight (8) 0.5" Holes @ 12010-12012' (SQZ'D Away 17 SKS)
Top of 5" Liner @ 12028'

7", 26#/29#, N-80 CSG @ 12046'
CMT'D w/ 1200 SKS VHT CMT

5" Perfs: 0.25", (120) Round HPF @ 12046-12433'

Top of 3.5" Liner @ 12418'

5", 18#, N-80 Liner @ 12434'

3.5" Perfs:
2.5" x 60M, 12R Slots @ 12420-12637'

3.5" Liner @ 12638'

Operator: Aera Energy LLC

Lease: Lloyd Corp.
Well Type: Producer
Status: Operational
Flood: ESDB
Base of Fresh Water: No
Directional: No

GL Elevation: 1198.3' asl
Datum to GL: 11.5' DF

Drill Date: 6/21/1955

Junk: Baker Model D Packer @
11963' (Unable to Pull)

Wellbore History

Orig. Hole (OH) TD @ 14045'
(See Lloyd Corp. 75 OH)
RD KOP @ 9290' into this wellbore
TD @ 12641'

Notes

Well originally completed w/ TD @ 12437'. Drilled past 5" Liner shoe, deepened well from 12437' to 12641' & ran 3.5" Liner on 5/9/1956.

Top of Zone Markers

A-A	3064'	AK-C	8437'
B-A	3276'	AM-C	8614'
D-A	3602'	AA-D	8940'
E-A	3804'	AC-D	9215'
F-A	3973'	AE-D	9401'
G-A	4164	AK-D	9744'
H-A	4250'	AM-D	9886'
J-A	4436'	AO-D	10125'
L-A	4545'	AP-D	10295'
M-A	4739'	AR-D	10415'
N-A	4869'	AS-D	10510'
O-A	5013'	AT-D	10685'
P-A	5211'	AU-D	10872'
R0-C	5585'	AU1-D	11045'
S-C	5720'	AV-D	11170'
S0-C	6279'	AX-D	11410'
Ua-C	6497'	DC-D	11703'
U-C	6602'	DD-D	11725'
V-C	6821'	DE-D	11790'
X2-C	7024'	DF-D	11838'
AA-C	7477'	DH-D	11910'
AC-C	7609'	DL-D	12110'
AE-C	7852'	DO-D	12267'
AG-C	8241'	DR-D	12410'

Prepared by: MJM (10/2/2013)
Updated by: LD (1/2/2014)
Updated by: J. Kahler (05/16/2016)

InterAct
