
DESERT GLOW 24

Deviated (15° to 30°), Sidetrack 1, 2/2/2023 9:38:49 AM

MD (ftKB)	Incl (°)	TVD (ftKB)	Zones	Top Zon
0	0.0	0.0		
50.0	0.4	50.0		
100.0	0.8	100.0		
150.0	2.9	150.0		
200.0	4.5	199.9		
250.0	6.1	249.8		
300.0	8.1	299.3		
350.0	9.7	348.6		
400.0	11.3	397.8		
450.0	12.9	446.7		
500.0	14.2	495.3		
550.0	15.0	543.7		
600.0	15.4	591.9		
650.0	15.6	640.1		
700.0	15.7	688.2		
750.0	15.8	736.4		
800.0	15.8	784.5		
850.0	15.8	832.6		
900.0	15.9	880.7		
950.0	16.1	928.7		
1,000.0	16.3	976.8		
1,050.0	16.4	1,024.7		
1,100.0	16.5	1,072.7		
1,150.0	16.6	1,120.6		
1,200.0	16.7	1,168.5		
1,250.0	16.7	1,216.4		

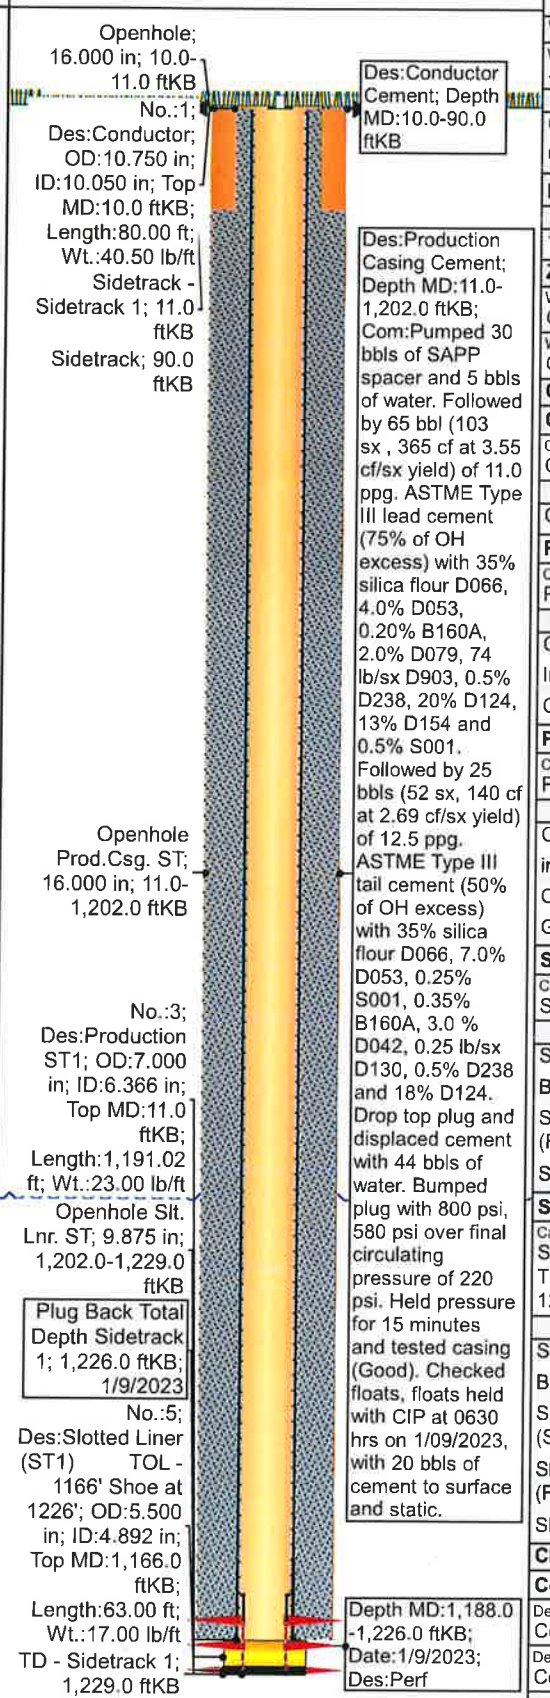

Well Header Setup

KB Datum Elevation (ft)	Spud Date	Rig Release Date
843.00	3/13/2006 20:00	1/10/2023 14:30

KB-Grd (ft)	Total Depth (All) (ftKB)
10.00	Original Hole - 1,216.0; Sidetrack 1 - 1,229.0

Well Name	API/UWI	Surface Legal Location
DG 24	0403029604-01	Sec14 T27S R27E MDBM

WELLBORE SECTIONS

Wellbore Name	Parent Wellbore	VS Dir (°)
Sidetrack 1	Original Hole	288.43

Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Openhole Prod.Csg. ST	16	11.0	1,202.0
Openhole Slt. Lnr. ST	9 7/8	1,202.0	1,229.0

Plug Back Total Depths

Date	Depth (ftKB)	Type	Com
1/9/2023	1,226.0	Top of shoe	Steel ball landed on top of shoe.

Zones

Wellbore Name	Zone Name	Top Depth (ftKB)	Reference Depth (ftKB)
Original Hole	Basal Etchegoin	1,056.0	
Original Hole	Chanac	1,159.0	

CASING DATA

Conductor

Casing Description	Run Date	Pull Date	Set Depth (ftKB)
Conductor	3/1/2006		90.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Conductor	10.750	10.050	80.00	J-55	40.50	10.0	90.0

Production Casing

Casing Description	Run Date	Pull Date	Set Depth (ftKB)
Production Casing	3/14/2006		1,090.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Casing Joints	7.000	6.366	929.99	J-55	23.00	130.0	1,060.0
Insert	7.000	6.366	0.01	J-55	23.00	1,060.0	1,060.0
Casing Joints	7.000	6.366	30.00	J-55	23.00	1,060.0	1,090.0

Production ST1

Casing Description	Run Date	Pull Date	Set Depth (ftKB)
Production ST1	1/9/2023		1,202.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Casing Joints	7.000	6.366	1,126.68	J-55	23.00	11.0	1,137.7
insert	7.000	6.366	0.10	J-55	23.00	1,137.7	1,137.8
Casing Joints	7.000	6.366	63.24	K-55	23.00	1,137.8	1,201.0
Guide Shoe	7.000	6.366	1.00	J-55	23.00	1,201.0	1,202.0

Slotted Liner

Casing Description	Run Date	Pull Date	Set Depth (ftKB)
Slotted Liner	7/16/2011		1,216.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
SSA	5.500	4.892	2.00	J-55	17.00	1,047.0	1,049.0
Blank Liner	5.500	4.892	37.00	J-55	17.00	1,049.0	1,086.0
Slotted Liner (Full Slots)	5.500	4.892	126.00	J-55	17.00	1,086.0	1,212.0
Spade Shoe	5.500	4.892	4.00	J-55	17.00	1,212.0	1,216.0

Slotted Liner (ST1) TOL - 1166' Shoe at 1226'

Casing Description	Run Date	Pull Date	Set Depth (ftKB)
Slotted Liner (ST1) TOL - 1166' Shoe at 1226'	1/10/2023		1,229.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
SSA	5.500	4.892	2.00	J55	17.00	1,166.0	1,168.0
Blank Liner	5.500	4.892	20.00	J55	17.00	1,168.0	1,188.0
Slotted Liner (Semi Slots)	5.500	4.892	10.00	J55	17.00	1,188.0	1,198.0
Slotted Liner (Full Slots)	5.500	4.892	28.00	J55	17.00	1,198.0	1,226.0
Shoe	5.500	4.892	3.00	J55	17.00	1,226.0	1,229.0

CEMENT DATA

Conductor, 90.0ftKB


Description	String	Type
Conductor Cement	Conductor, 90.0ftKB	Casing

Description	Top Depth (ftKB)	Bottom Depth (ftKB)	Vol Cement Rel (bbl)
Conductor Cement	10.0	90.0	0.0

DESERT GLOW 24

Deviated (15° to 30°), Sidetrack 1, 2/2/2023 9:38:50 AM

MD (ftKB)	Incl (°)	TVD (ftKB)	Zones	Top Zon
0	0.0	0		
50	0.4	50		
100	0.8	100		
150	2.9	150		
200	4.5	199.8		
250	6.1	249.6		
300	8.1	299.3		
350	9.7	348.6		
400	11.3	397.8		
450	12.9	446.7		
500	14.2	495.3		
550	15.0	543.7		
600	15.4	591.9		
650	15.6	640.1		
700	15.7	688.2		
750	15.8	736.4		
800	15.8	784.5		
850	15.8	832.6		
900	15.9	880.7		
950	16.1	928.7		
1,000	16.3	976.8		
1,050	16.4	1,024.7		
1,100	16.5	1,072.7		
1,150	16.6	1,120.6		
1,200	16.7	1,168.5		
1,250	16.7	1,216.4		

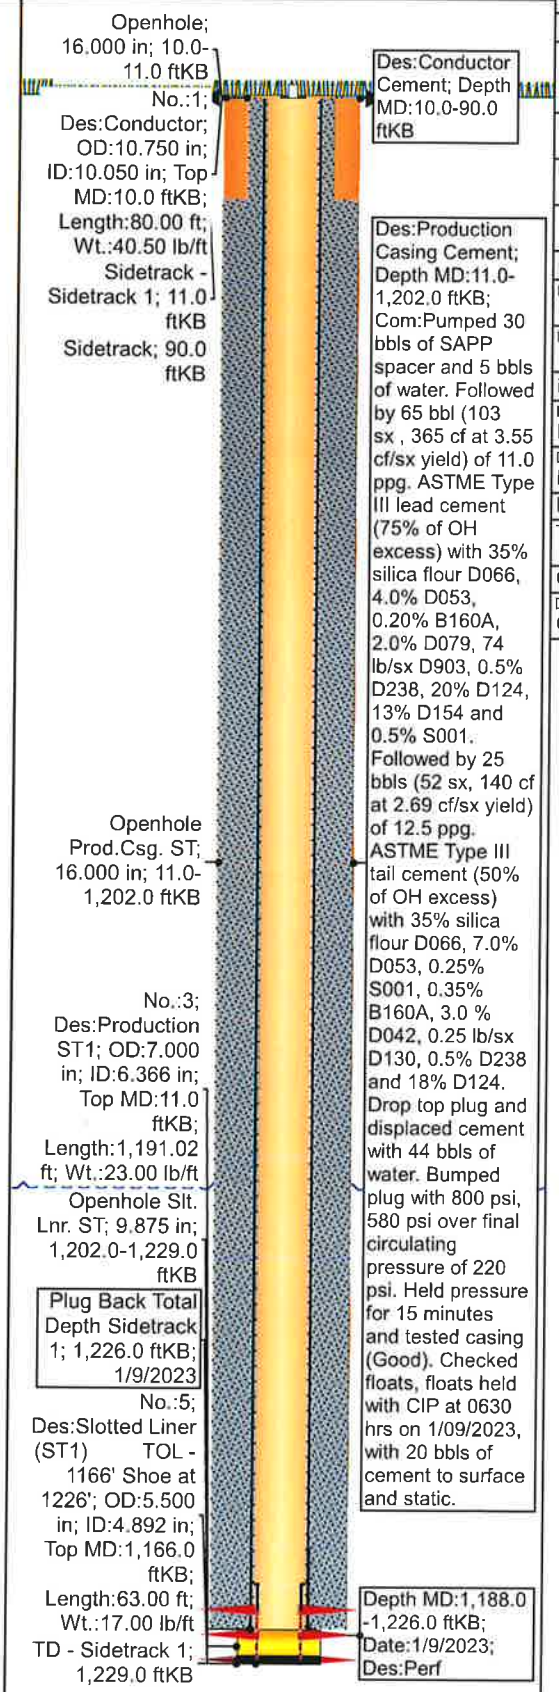

CEMENT DATA

Production Casing, 1,090.0ftKB

Description	String	Type
Production Casing Cement	Production Casing, 1,090.0ftKB	Casing

Description	Top Depth (ftKB)	Bottom Depth (ftKB)	Vol Cement Ret (bbl)
Production Casing Cement	130.0	1,090.0	15.0

Production Casing, 1,090.0ftKB

Description	String	Type
Abandonment Plug	Production Casing, 1,090.0ftKB	Plug

Description	Top Depth (ftKB)	Bottom Depth (ftKB)	Vol Cement Ret (bbl)
Abandonment Plug	992.0	1,200.0	0.0
Abandonment Plug	185.0	992.0	0.0
Abandonment Plug	137.0	185.0	0.0

Original Hole

Description	String	Type
Cement KO Plug	Original Hole	Plug

Description	Top Depth (ftKB)	Bottom Depth (ftKB)	Vol Cement Ret (bbl)
Cement KO Plug	130.0	137.0	0.0

Production ST1, 1,202.0ftKB

Description	String	Type
Production Casing Cement	Production ST1, 1,202.0ftKB	Casing

Description	Top Depth (ftKB)	Bottom Depth (ftKB)	Vol Cement Ret (bbl)
Production Casing Cement	11.0	1,202.0	20.0

PERFORATION DATA

Type	Top Depth (ftKB)	Btm (ftKB)	Shot De...	Comment
	1,188.0	1,226.0		Slotted liner 1188' - 1226'

Other In Hole

Description	Run Date	Pull Date	Top (ftKB)	Btm (ftKB)	ID (in)
Gravel packs	1/9/2023		1,202.0	1,229.0	5.50
