
Wellbore Diagram

Well Name: FA GD-3 **API: 0403048164**

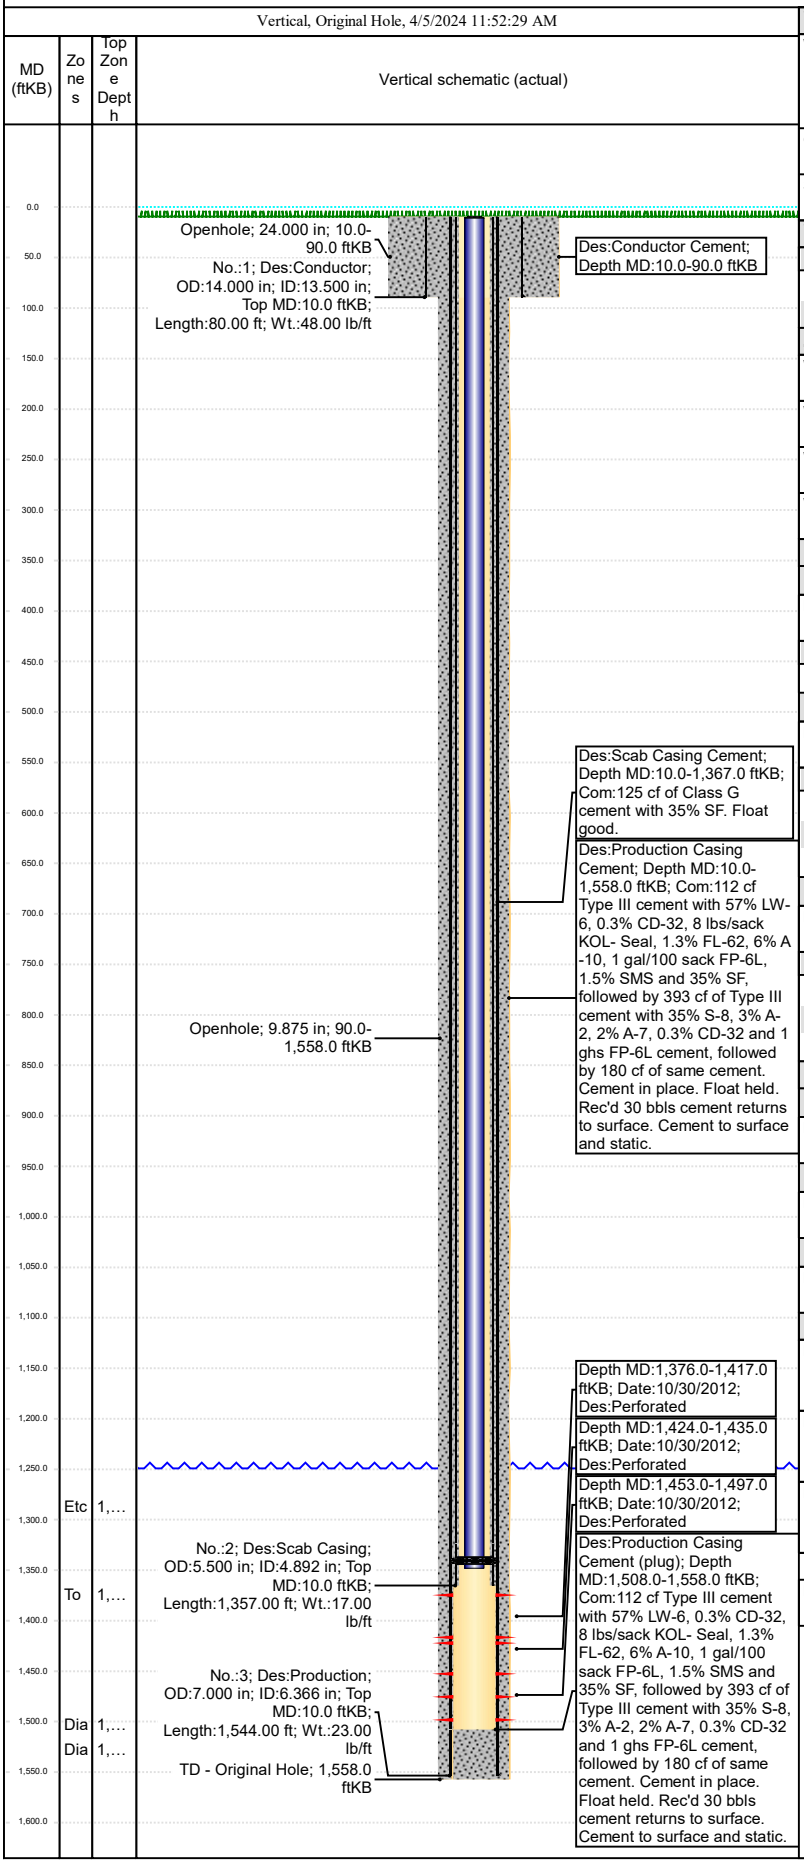

Well Header Setup

Well Name	Field Name	API/UWI (10)	PBTD (ftKB)	TD (max) (ftKB)
FA GD-3	Midway Sunset MNDI RPT	0403048164		1,558.0

Gr Elev (ft)	KB-Grd (ft)	Spud Date	Rig Release Date	Abandon Date
1,237.00	10.00	10/12/2012	10/14/2012	

Section	Township	Range	Meridian	Latitude (NAD 27) (°)	Longitude (NAD 27) (°)	Datum
11	31S	22E	MD	35.2500877400	-119.5735549900	NAD 83

WELLBORE SECTIONS

Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Openhole	24	10.0	90.0
Openhole	9 7/8	90.0	1,558.0

Zones

Wellbore Name	Zone Name	Top Depth (ftKB)	Reference Depth (ftKB)
Original Hole	Etchegoin_UCL	1,289.0	0.0
Original Hole	Top Potter	1,375.0	
Original Hole	Diatomite	1,505.0	
Original Hole	Diatomite_LCL	1,530.0	

CASING DATA

Conductor

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
9/10/2012	14	13.50	H-40	48.00	10.0	90.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Conductor	14.000	13.500	80.00	H-40	48.00	10.0	90.0

Scab Casing

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
1/24/2018	5 1/2	4.89	J-55	17.00	10.0	1,367.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Casing Joints	5.500	4.892	1,314.00	J-55	17.00	10.0	1,324.0
Float Collar	5.500	4.892	1.00	J-55	17.00	1,324.0	1,325.0
Shoe Track	5.500	4.892	42.00	J-55	17.00	1,325.0	1,367.0

Production

Run Date	OD (in)	ID (in)	String Grade	Wt/Len (lb/ft)	Top (ftKB)	Set Depth (ftKB)
10/14/2012	7	6.37	J-55	23.00	10.0	1,554.0

Item Des	OD (in)	ID (in)	Len (ft)	Grade	Wt (lb/ft)	Top (ftKB)	Btm (ftKB)
Casing Joints	7.000	6.366	1,498.00	J-55	23.00	10.0	1,508.0
Insert float	7.000	6.366	1.00	J-55	23.00	1,508.0	1,509.0
Shoe Track	7.000	6.366	45.00	J-55	23.00	1,509.0	1,554.0

CEMENT DATA

Conductor , 90.0 ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full Ret...	Vol...
Conductor Cement	Casing	10.0	90.0	No	0.0

Production , 1,558.0 ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full Ret...	Vol...
Production Casing Cement	Casing	10.0	1,558.0	Yes	30.0

Scab Casing , 1,367.0 ftKB

Description	Type	Top (ftKB)	Btm (ftKB)	Full Ret...	Vol...
Scab Casing Cement	Casing	10.0	1,367.0	No	0.0

PERFORATION DATA

Date	Type	Top (ftKB)	Btm (ftKB)	Entered Sho...	Calculated...	Comment
10/30/2012	Perforated	1,376.0	1,417.0	328	328	8 JSPF
10/30/2012	Perforated	1,424.0	1,435.0	88	88	8 JSPF
10/30/2012	Perforated	1,453.0	1,497.0	352	352	8 JSPF

Other In Hole

Des		OD (in)	ID (in)	Top (ftKB)	Btm (ftKB)	Comment
